



Department of Administration
Purchasing Division
2019 Washington Street East
Post Office Box 50130
Charleston, WV 25305-0130

State of West Virginia Purchase Order

Order Date: 12-15-2021

CORRECT ORDER NUMBER MUST APPEAR
ON ALL PACKAGES, INVOICES, AND
SHIPPING PAPERS. QUESTIONS
CONCERNING THIS ORDER SHOULD BE
DIRECTED TO THE DEPARTMENT
CONTACT.

Order Number:	CPO 0310 6377 DNR2000000012 6	Procurement Folder:	697731
Document Name:	Bowden Hatchery 3 - New Facilities Construction	Reason for Modification:	Change Order No. 04 to extend and decrease the contract per the attached documentation.
Document Description:	Change Order No. 04- Bowden Hatchery 3- New Facilities Const		
Procurement Type:	Central Purchase Order		
Buyer Name:	Joseph E Hager III		
Telephone:	(304) 558-2306		
Email:	joseph.e.hageriii@wv.gov		
Shipping Method:	Best Way	Effective Start Date:	2020-08-31
Free on Board:	FOB Dest, Freight Prepaid	Effective End Date:	2022-06-03

VENDOR	DEPARTMENT CONTACT																				
Vendor Customer Code: 000000201679 BRECKENRIDGE CORP PO BOX 247 BUCKHANNON WV 262010247 US Vendor Contact Phone: 304-472-3350 Extension: Discount Details: <table><thead><tr><th></th><th>Discount Allowed</th><th>Discount Percentage</th><th>Discount Days</th></tr></thead><tbody><tr><td>#1</td><td>No</td><td>0.0000</td><td>0</td></tr><tr><td>#2</td><td>Not Entered</td><td></td><td></td></tr><tr><td>#3</td><td>Not Entered</td><td></td><td></td></tr><tr><td>#4</td><td>Not Entered</td><td></td><td></td></tr></tbody></table>		Discount Allowed	Discount Percentage	Discount Days	#1	No	0.0000	0	#2	Not Entered			#3	Not Entered			#4	Not Entered			Requestor Name: James H Adkins Requestor Phone: (304) 558-3397 Requestor Email: jamie.h.adkins@wv.gov 22 FILE LOCATION _____
	Discount Allowed	Discount Percentage	Discount Days																		
#1	No	0.0000	0																		
#2	Not Entered																				
#3	Not Entered																				
#4	Not Entered																				

INVOICE TO	SHIP TO
DIVISION OF NATURAL RESOURCES PARKS & RECREATION-PEM SECTION 324 4TH AVE SOUTH CHARLESTON WV 25305 US	DIVISION OF NATURAL RESOURCES BOWDEN HATCHERY RT 1, BOX 80 ELKINS WV 26241 US

12-17-21
B&F

Purchasing Division's File Copy

Total Order Amount: \$6,652,041.00

ENTERED

PURCHASING DIVISION AUTHORIZATION DATE: <i>Lynnda Harper 12/17/21</i> ELECTRONIC SIGNATURE ON FILE	ATTORNEY GENERAL APPROVAL AS TO FORM DATE: <i>John S. Graw</i> ELECTRONIC SIGNATURE ON FILE	ENCUMBRANCE CERTIFICATION DATE: <i>Beverly Tiden 12-17-21</i> ELECTRONIC SIGNATURE ON FILE
--	---	--

12/17/2021

Extended Description:

Change Order

Change Order No. 04 is issued to extend and decrease the original contract according to all terms, conditions, and specifications contained in the original contract including all authorized change orders. The contract (unit prices, hourly rates, annual fee, etc.) is decreased as defined in the attached documentation.

Dates of extension: 04/23/2022 - 06/03/2022.

Original Contract Price: \$6,366,000.00

Change Order No. 02 Increase: \$ 180,000.00

Change Order No. 03 Increase: \$ 160,494.00

Change Order No. 04 Decrease: (\$ 54,453.00)

Contract New Total: \$6,652,041.00

Effective: 05/20/2021

All provisions of the original Contract and subsequent Change Orders not modified herein shall remain in full force and effect.

No other changes.

Line	Commodity Code	Quantity	Unit	Unit Price	Total Price
1	72120000	0.00000		0.000000	6366000.00
Service From	Service To	Manufacturer	Model No		
2020-08-31	2022-06-03				

Commodity Line Description: Building Construction Services

Extended Description:

Construction of new facilities at Bowden Hatchery.

Line	Commodity Code	Quantity	Unit	Unit Price	Total Price
2	72120000	0.00000		0.000000	180000.00
Service From	Service To	Manufacturer	Model No		
2020-08-31	2022-06-03				

Commodity Line Description: Change Order No. 02

Extended Description:

Construction of new facilities at Bowden Hatchery.

Line	Commodity Code	Quantity	Unit	Unit Price	Total Price
3	72120000	0.00000		0.000000	106041.00
Service From	Service To	Manufacturer	Model No		
2020-08-31	2022-06-03				

Commodity Line Description: Change Order No. 03 & No. 04

Extended Description:

Construction of new facilities at Bowden Hatchery.

Change Order No. 03 \$160,494.00

Change Order No. 04 (\$54,453.00)

Approved
12/14/21

**DIVISION OF NATURAL RESOURCES
PLANNING, ENGINEERING AND MAINTENANCE**
1194 Carnifex Ferry Road
Summersville, West Virginia 26651
Cell phone: 304-389-8597

Stephen S. McDaniel
Director

October 22, 2021

J. Adkins
Jamie Adkins
WV Division of Natural Resources
Property and Procurement Office
324 4th Avenue
South Charleston, WV 25303

Dear Mr. Adkins:

Re: Change Order No. 4 (Revised)
Bowden Fish Hatchery
Contract 3 – New Facilities
CPO 0310 6377
DNR 2000000012

Change Order No. 4 is being submitted to address modifications to the project scope and includes the following: extension of the length of electrical service, make minor piping changes, raise elevation of drum filter openings in concrete wall, make clarifier modifications, addition of fish screens to properly install the new low head oxygenators, modify the DO/PH instrument mountings, delete the original bird netting pay item, replace the existing flood pump engine, installation of slide gate. The net change order amount will result in a deduction of \$54,453.00. The contract time will be extended 42 days to allow time for additional work and for supply chain delays affecting delivery of materials.

I recommend the change order request be approved.

Please contact me should you have questions or need additional information.

Sincerely,

Mark R. Proctor
Project Engineer
WV Division of Natural Resources

cc: Brad Leslie, Chief Engineer
Rebecca Westfall, Administrative Services Assistant



**Chapman
Technical
Group**
a division of
GRW

June 25, 2021

Mr. Mark Proctor
WV Division of Natural Resources
324 4th Avenue
South Charleston, West Virginia 25303

**Re: Bowden Hatchery
Contract 3
Hatchery Improvements**

Dear Mr. Proctor:

As the construction of Contract 3 progresses, the following issues have arisen and need to be addressed by change order.

1. The Power Company has advised that new electrical service is required to come from a source more distant than originally anticipated and as bid by the Contractor. Additional conduit and electrical gear is required.
2. Two minor piping changes need to be made due to adjustments necessary to accommodate actual installed equipment and piping.
3. Openings in the concrete walls for the drum filter need to be raised to accommodate actual installed equipment and piping.
4. Modifications to the clarifier are required due to differing site conditions. The clarifier was raised slightly to avoid poor soils.
5. Final configuration of the Low Head Oxygenators (LHO) have dictated that an adjustment to the screens in the raceways be made. As a result, additional screens are required beyond what was included in the bid in order to properly install the LHOs.
6. Modifications to the DO/PH instrument mountings are required to accommodate new equipment but resulted in a less expensive installation.
7. It has been determined by the Owner that the bird netting is not essential to the project and shall be deleted for a cost savings.
8. It has been determined that the existing flood pump engine is nearing the end of its useful life and should be replaced in order to maintain efficient long-term operation of the hatchery.
9. After construction began a more thorough evaluation of the flood pump station was able to be performed and it was determined that replacing the flex valve as originally called for will not allow for optimum operation of the hatchery treatment systems and the flood pump. A new slide gate should be installed instead will allow for more efficient operation.

200 Sixth Avenue
Saint Albans, WV 25177

304.727.5501
304.727.5580 Fax

Buckhannon, WV
Lexington, KY

www.chaptech.com




Mr. Mark Proctor
June 25, 2021
Page Two

We believe that the proposed costs for the change order are fair and reasonable. The pertinent documents to process the change order are enclosed. If you have questions or need additional information, please contact me.

Sincerely,

CHAPMAN TECHNICAL GROUP



Joseph E. Byrd, ASLA

BRECKENRIDGE

October 7, 2021
Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177


Att: Mr. Joe Bird, P.L.A, A.S.I.A
Re: WVDNR Bowden Fish Hatchery Contact 3 - New Facilities
Change Order Proposal - Request For Additional Time in CO 4

Dear Mr. Bird,

Please add a total of 42 days to the contract for the procurement of materials and work involving CO Proposals which were incorporated into Change Order 4. This will make a grand total of a 42 day time extension for Change Order 4.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION



Eric J. Andrew
Project Manager

EJA
cc: file



Document G701™ – 2017

Change Order

PROJECT: (Name and address)
Bowden Hatchery 3 - New Facilities
Construction
Building Hatchery
Rt. 1 Box 60
Elkins, WV 26241

CONTRACT INFORMATION:
Contract For: Hatchery Facilities
Upgrades
CPO 0310 6377
DNR 2000000012

CHANGE ORDER INFORMATION:
Change Order Number: 004

Date: July 16, 2020

Date: October 19, 2021

OWNER: (Name and address)
WV Division of Natural Resources
Parks and Recreation - PEM Section
324 4th Ave.
South Charleston, WV 25303

ARCHITECT: (Name and address)
Chapman Technical Group
200 Sixth Avenue
Saint Albans, WV 25177

CONTRACTOR: (Name and address)
Breckenridge Corporation
PO Box 247
Buckhannon, WV 26201

THE CONTRACT IS CHANGED AS FOLLOWS:

(Insert a detailed description of the change and, if applicable, attach or reference specific exhibits. Also include agreed upon adjustments attributable to executed Construction Change Directives.)

- | | |
|--|-----------------|
| 1. New electrical service for Treatment Building. | \$ 40,691.00 |
| 2. Piping changes due to changing conditions. | \$ 3,650.00 |
| 3. Raise openings in drum filter sumps due to changing conditions. | \$ 1,000.00 |
| 4. Clarifier modifications. | \$ 6,690.00 |
| 5. Additional screens in existing raceways | \$ 14,741.00 |
| 6. DO and PH meter modifications. | \$ (525.00) |
| 7. Delete bird netting for existing raceways. | \$ (207,500.00) |
| 8. Flood pump engine replacement. | \$ 53,700.00 |
| 9. New slide gate at pump station. | \$ 33,100.00 |

Total: \$ (54,453.00)

The original Contract Sum was	\$ 6,366,000.00
The net change by previously authorized Change Orders	\$ 340,494.00
The Contract Sum prior to this Change Order was	\$ 6,706,494.00
The Contract Sum will be decreased by this Change Order in the amount of	\$ 54,453.00
The new Contract Sum including this Change Order will be	\$ 6,652,041.00

The Contract Time will be increased by forty-two (42) days.
The new date of Substantial Completion will be June 3, 2022.

NOTE: This Change Order does not include adjustments to the Contract Sum or Guaranteed Maximum Price, or the Contract Time, that have been authorized by Construction Change Directive until the cost and time have been agreed upon by both the Owner and Contractor, in which case a Change Order is executed to supersede the Construction Change Directive.

NOT VALID UNTIL SIGNED BY THE ARCHITECT, CONTRACTOR AND OWNER.

Chapman Technical Group
ARCHITECT (Firm name)

SIGNATURE

Joseph E. Bird
Senior Vice President

PRINTED NAME AND TITLE

DATE

10-19-2021

Breckenridge Corporation
CONTRACTOR (Firm name)

SIGNATURE

Keith Skelton
Project Manager

PRINTED NAME AND TITLE

DATE

10/19/21

WV Division of Natural Resources
OWNER (Firm name)

SIGNATURE

Stephen S. McDaniel
Director

PRINTED NAME AND TITLE

DATE

11/16/2021



GENERAL CONTRACTORS

April 1, 2021
Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177

Att: Mr. Joe Bird, PLA, ASLA
Re: WVDNR Bowden Fish Hatchery Improvements Contract 3
Change Order Proposal # 15 Primary Service For Treatment Bldg

Dear Mr. Bird,

As previously discussed, we are pleased to provide the following change order proposal #10 to install the required conduit, trenching, transformer pad, & switchgear for the planned Treatment Bldg 400 amp 480/277v 3 phase service. The 1395' route for primary power is per attached map.

We propose to perform the above work for the lump sum price of **\$40,691.00 (Forty Thousand Six Hundred Ninety-One Dollars)** (Please see attached breakdown for more information).

If acceptable, please issue a change order in the above amount and add four (4) days to the contract time. This proposal only includes those items described above and included herein and doesn't include any unforeseen conditions.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION

Eric J. Andrew
Project Manager


EJA
cc: file
attach: Cost breakdown 04/01/21 (2 pgs)
Map for primary route (1pg)

Legend 1395' UG primary

 Bowden State Fish Hatchery

 Pull Box

 Transformer

 UG Primary Power 1395'



BRECKENRIDGE

GENERAL CONTRACTORS

March 12, 2021

Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177

Att: Mr. Joe Bird, PLA, ASLA
Re: WVDNR Bowden Fish Hatchery Contract 3 - New Facilities
Change Order Proposal # 13 - Pipe Modifications created by Subm 42 Eng'r review comments

Dear Mr. Bird,

As per the Engineer's review comments in Approved Submittal #42 (Pipe Dwgs 10-13), we are pleased to provide the following change order proposal to make the appropriate changes required by the engineers comments as generally described below:

1) Pipe Dwg 11 Comment "Locate Flow Meter at Elevation 2195.50". The contract dwgs showed the flow meter attaching to the 12" flanged wye assembly. Locating the flow meter at the requested elevation will create an additional 12" flanged spool piece between the flow meter and the wye assy. This is typical at 4 ea recycle headboxes. This wasn't included in COP 12 raising headboxes.

2) Pipe Dwg 10 Comment wants to change the 24x12 DI MJ concentric reducer to an eccentric reducer to deter air entrapment. This eccentric reducer is not made in ductile iron. In order to make this change to an eccentric reducer, we will have to change the 24x12 DI MJ reducer to a 24x12 sdr35 pvc eccentric reducer. This will also involve adding a 24" and 12" mj x sdr35 transition gasket and a 12" mj solid sleeve. Please note: fittings in this area had to be changed to ductile iron, because there wasn't enough room for the pvc fittings due to the lay lengths.

We propose to perform the above work for the lump sum price of **\$3,650.00 (Three Thousand six hundred fifty dollars)** (Please see attached breakdown for more information).

If this proposal is acceptable, Please issue a change order in the above amount and add one (1) day to the contract time. Please advise on this change order proposal as soon as possible, so we know how to proceed. This proposal only includes those items described above and included herein and doesn't include any unforeseen conditions. This proposal is good for 28 days and is subject to change after said date.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION


Keith E. Skelton
Project Manager

KLS
cc: file
attach: Cost breakdown-03/12/21 (2 pgs)

CONTRACTOR'S LICENSE
WV 001651

P.O. BOX 247 • BRICKYARD ROAD
BUCKHANNON, WV 26201

PHONE (304) 472-3350
FAX (304) 472-8506

BRECKENRIDGE CORP.

BOWDEN FISH HATCHERY NEW FACILITIES COP

DATE 12-Mar-21

DESCRIPTION	KLS	WVDNR BOWDEN FISH HATCHERY New Facilities cop 13	JOB TOTALS			SHT 1 OF 1
COP 13 - Modifi due to Subm 42 rwr comments			MATL	LABOR	EQUIP	COMMENTS
			2,939	0	0	2,939

0 % LABOR ESCALATION	SUBTOTAL	2,939	0	0	0	2,939
0 % MATERIAL ESCALATION	SUBTOTAL	0	0	0	0	0
61 % SALES TAX ON MATERIALS	SUBTOTAL	2,939	0	0	0	2,939
32 % LABOR BURDEN	SUBTOTAL	176	0	0	0	176
	SUBTOTAL	3,115	0	0	0	3,115
0 % PD & PL INSURANCE	SUBTOTAL	0	0	0	0	0
0 % BUILDERS' RISK INSURANCE	SUBTOTAL	23	0	0	0	23
PERFORMANCE BOND	SUBTOTAL	3,138	0	0	0	3,138
0 % B&O TAX	SUBTOTAL	36	0	0	0	36
	SUBTOTAL	3,174	0	0	0	3,174
15 % OVERHEAD & ADMINISTRATIVE	SUBTOTAL	478	0	0	0	478
0 % MARKUP	SUBTOTAL	3,650	0	0	0	3,650
	SUBTOTAL	0	0	0	0	0
	BID TOTAL	3,650	0	0	0	3,650
	Total	3,650	0	0	0	3,650

12-Mar-21

6:50

SHEET NO. 1

BRECKENRIDGE

GENERAL CONTRACTORS

March 17, 2021

Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177

Att: Mr. Joe Bird, PLA, ASLA
Re: WVDNR Bowden Fish Hatchery Contract 3 - New Facilities
Change Order Proposal # 14 - Change opening elevation in Drum Filter Sump Interior walls

Dear Mr. Bird,

As directed, we are pleased to provide the following change order proposal to raise the openings in the concrete side walls of the drum filter sumps 2.5-inches (from 2180.08 to 2180.29). This change includes modifying the resteel as required to fit the new openings.

We propose to perform the above work for the lump sum price of \$1,000.00 (One Thousand dollars) (Please see attached breakdown for more information).

As directed, Please issue a change order in the above amount and add one (1) day to the contract time. This proposal only includes those items described above and included herein and doesn't include any unforeseen conditions.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION



Keith L. Skelton
Project Manager

KLS
cc: file
attach: Cost breakdown 03/17/21 (2 pgs)

BOWDEN FISH HATCHERY NEW FACILITIES COP

KLS		WYDNR BOWDEN FISH HATCHERY New Facilities Exp 14				SHT 1 OF 1
DESCRIPTION	JOB TOTALS			TOTAL	COMMENTS	
	MATL	LABOR	EQUIP			
COP 14 - Change wall opening in treatment bldg off trt walls	326	350	0	0		

0	% LABOR ESCALATION	325	350	0	0	675
0	% MATERIAL ESCALATION	0	0	0	0	0
	SUBTOTAL	325	350	0	0	675
61	% SALES TAX ON MATERIALS	20				20
32	% LABOR BURDEN	345	112	0	0	112
	SUBTOTAL	345	462	0	0	607
	% PD & PL INSURANCE					32
						838
	SUBTOTAL					21
	% BUILDERS' RISK INSURANCE					660
	SUBTOTAL					10
	PERFORMANCE BOND					870
0	% B&O TAX					0
	SUBTOTAL					870
15	% OVERHEAD & ADMINISTRATIVE					130
	SUBTOTAL					1,000
0	% MARKUP					0
	SUBTOTAL					1,000
	BID TOTAL					4,000

SHEET NO. 1

BRECKENRIDGE

GENERAL CONTRACTORS

April 22, 2021

Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177

Att: Mr. Joe Bird, PLA, ASLA
Re: WVDNR Bowden Fish Hatchery Contract 3 - New Facilities
Change Order Proposal # 16 - Relocate Clarifier PRV's and Change Clarifier Effluent pipe to DI

Dear Mr. Bird,

As directed by email dated March 23, 2021 and at the April 7, 2021 job meeting, we are pleased to provide the following change order proposal to relocate the 2 each 4" wall type pressure relief valves in the clarifier to 2-foot above the floor slab and to change the above grade clarifier effluent piping from pvc to ductile iron (see attached sketch)

We propose to perform the above work for the lump sum price of \$6,690.00 (Six Thousand Six Hundred Ninety dollars) (Please see attached breakdown for more information).


Please issue a change order in the above amount and add two (2) days to the contract time. This proposal only includes those items described above and included herein and doesn't include any unforeseen conditions. This proposal is good for 28 days and is subject to change after said date.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION


Keith L. Skelton
Project Manager

KLS
cc: file
attach: Cost breakdown 04/22/21 (2 pgs)
Sketch 4/22/21 (1 pg)

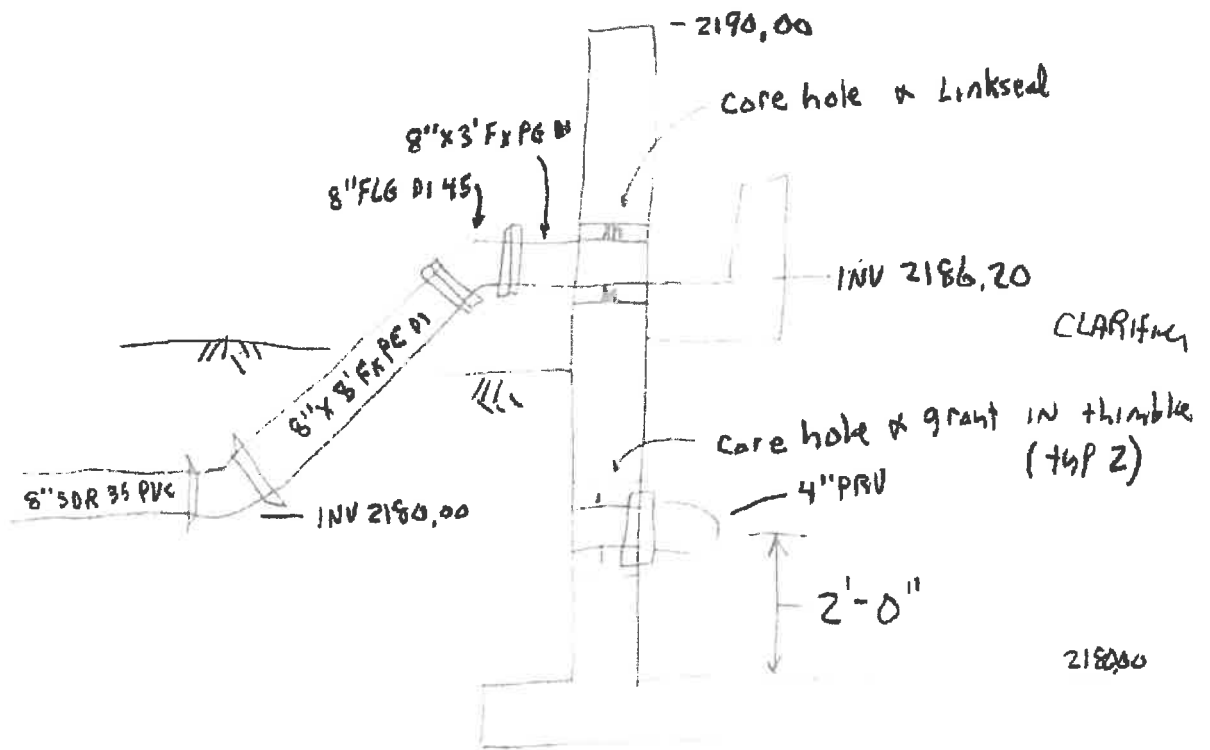

Bowden
 COP 16 sketch
 KCS 4/22/21

BRECKENRIDGE CORP.

BOWDEN FISH HATCHERY NEW FACILITIES COP

DATE 22-Apr-21

CLS	DESCRIPTION	MATL	LABOR	EQUIP	SUB	TOTAL	SHT 1 OF 1
	COP 16 - Replaces RV's at Clarifier & Change Clarifier	2,728	1,950	0	60	4,738	
	Effluent piping to Di						

	SUBTOTAL	2,728	1,950	0	60	4,738	
01 % LABOR ESCALATION			0			0	
01 % MATERIAL ESCALATION		0				0	
	SUBTOTAL	2,728	1,950	0	60	4,738	
01 % SALES TAX ON MATERIALS		164				164	
321 % LABOR BURDEN		2,892	2,574	0	60	5,528	
	SUBTOTAL					181	
						5,707	
						45	
						5,762	
						88	
						5,818	
						0	
						5,818	
15 % OVERHEAD & ADMINISTRATIVE						873	
						6,891	
01 % MARKUP						0	
						6,891	
	BID TOTAL					8,690	
						Total	

::

22-Apr-21

9:33

SHEET NO. 1

BRECKENRIDGE

GENERAL CONTRACTORS

April 22, 2021

Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177

Att: Mr. Joe Bird, PLA, ASLA
Re: WVDNR Bowden Fish Hatchery Improvements Contract 3
Change Order Proposal # 17 Add 4EA Screens, Guides, and Perf Plates

Dear Mr. Bird,


As previously discussed, we are pleased to provide the following change order proposal #17 to add 4EA aluminum screens, guides, and perforated plates to the existing 10/20/30/40 raceways. Please see breakdown for more information.

We propose to perform the above work for the lump sum price of **\$14,741.00 (fourteen thousand seven hundred forty-one dollars)** (Please see attached breakdown for more information).

If acceptable, please issue a change order in the above amount and add zero (0) weeks to the contract time. This proposal only includes those items described above and included herein and doesn't include any unforeseen conditions. This change order proposal is valid for seven (7) days and subject to review thereafter.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION


Eric J. Andrew
Project Manager

EJA
cc: file
attach: Cost breakdown 04/22/21 (2 pgs)

CONTRACTOR'S LICENSE
WV 001651

P.O. BOX 247 • BRICKYARD ROAD
BUCKHANNON, WV 26201

PHONE (304) 472-3350
FAX (304) 472-8506

BRECKENRIDGE CORP.

BOWDEN FISH HATCHERY NEW RACEWAYS CONT 3 COP17

DATE 22-Apr-21

WYDNR BOWDEN FISH HATCHERY New Facility							SHT 1 OF 1
EJA	DESCRIPTION	MATL	LABOR	EQUIP	SUB	TOTAL	COMMENTS
	COP 17 Add 4EA Sun Mount Screens and Guides ..Inc perf plates	11,125	600	25	0	11,750	
	<input type="checkbox"/> % LABOR ESCALATION						
	<input type="checkbox"/> % MATERIAL ESCALATION						
	SUBTOTAL	11,125	600	25	0	11,750	
	<input type="checkbox"/> % SALES TAX ON MATERIALS						
	<input checked="" type="checkbox"/> % LABOR BURDEN	11,125	600	25	0	11,750	
	SUBTOTAL	688	192			880	
	<input type="checkbox"/> % PD & PL INSURANCE	11,793	792	25	0	12,610	
	SUBTOTAL					40	
	<input type="checkbox"/> % BUILDERS' RISK INSURANCE					12,648	
	SUBTOTAL					23	
	<input type="checkbox"/> PERFORMANCE BOND					12,872	
	<input type="checkbox"/> % S&O TAX					146	
	SUBTOTAL					12,818	
	<input checked="" type="checkbox"/> % OVERHEAD & ADMINISTRATIVE					0	
	SUBTOTAL					1,823	
	<input type="checkbox"/> % MARKUP					14,741	
	SUBTOTAL					0	
	Bid TOTAL					14,741	
	Total					14,741	

BRECKENRIDGE

GENERAL CONTRACTORS

April 27, 2021

Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177

Att: Mr. Joe Bird, PLA, ASLA
Re: WVDNR Bowden Fish Hatchery Improvements Contract 3
Change Order Proposal # 18 Instrument Cables/Mounting, Stands Credit, & Nursery Genset
Trenching/Raceway Credit

Dear Mr. Bird,

As previously discussed, we are pleased to provide the following change order proposal #18 to extend DO/PH instrument cables and modify mounting. Also, included herein are credits for 2EA fabricated instruments stands at the PH transmitters and trenching/raceway credit for the Nursery Genset. Please see breakdown for more information.

We propose to perform the above work for the credit lump sum price of \$ -525.00 (negative five hundred twenty-five dollars) (Please see attached breakdown for more information).

If acceptable, please issue a change order in the above amount and add zero (0) weeks to the contract time. This proposal only includes those items described above and included herein and doesn't include any unforeseen conditions. This change order proposal is valid for seven (7) days and subject to review thereafter.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION


Eric J. Andrew
Project Manager

EJA
cc: file
attach: Cost breakdown_04/27/21 (2_pgs).

EJA		WOMR BOWDEN FISH HATCHERY New Ponds COP18					SHT 1 OF 1
DESCRIPTION	JOB TOTALS					COMMENTS	
	MATL	LABOR	EQUIP	SUB	TOTAL		
COP 18 Instrument Cables/Mounting/Stand a Credit & Credit for Nursery Genset Trench/Raceway	440	-500	-300	0	-360		

	BID TOTAL	Total
<input type="text"/> % LABOR ESCALATION		
<input type="text"/> % MATERIAL ESCALATION		
SUBTOTAL	440	-300
	0	0
SUBTOTAL	440	-300
<input type="text"/> % SALES TAX ON MATERIALS	26	26
<input type="text"/> % LABOR BURDEN		-180
SUBTOTAL	466	-494
<input type="text"/> % PD & PL INSURANCE		-33
SUBTOTAL		-527
<input type="text"/> % BUILDERS' RISK INSURANCE		7
SUBTOTAL		-519
<input type="text"/> PERFORMANCE BOND		-8
SUBTOTAL		-525
<input type="text"/> % B&O TAX		0
SUBTOTAL		-525
<input type="text"/> % OVERHEAD & ADMINISTRATIVE		0
SUBTOTAL		-525
<input type="text"/> % MARKUP		0
SUBTOTAL		-525

BRECKENRIDGE

GENERAL CONTRACTORS

April 27, 2021

Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177

Att: Mr. Joe Bird, PLA, ASLA
Re: WVDNR Bowden Fish Hatchery Improvements Contract 3
Change Order Proposal # 19 Delete Leaf Nets Ex Raceways 10/20/30/40

Dear Mr. Bird,

As previously discussed, we are pleased to provide the following change order proposal #19 to delete the leaf net structures at existing raceways series 10/20/30/40. This price is less a 2500.00 cost for misc metals shop drawings that had to be paid to the supplier.

We propose to perform the above work for the credit lump sum price of \$ -207,500.00 (negative two hundred seven thousand five hundred dollars).

If acceptable, please issue a change order in the above amount and add zero (0) weeks to the contract time. This proposal only includes those items described above and included herein and doesn't include any unforeseen conditions. This change order proposal is valid for seven (7) days and subject to review thereafter.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION



Eric J. Andrew
Project Manager

EJA
cc: file

BRECKENRIDGE

GENERAL CONTRACTORS

April 29, 2021

Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177

Att: Mr. Joe Bird, PLA, ASLA
Re: WVDNR Bowden Fish Hatchery Improvements Contract 3
Change Order Proposal # 20 Flood Pump Engine Replacement

Dear Mr. Bird,


As previously discussed, we are pleased to provide the following change order proposal #20 to replace the LPG engine package on the existing flood pump. We will furnish and install IEA Husker Power Products GM 4.3 liter unit. The unit will be skid mounted and include belt and sheave with new PTO shaft for connection to the existing Crisafulli pump. Controls will be via Controls Inc. panel and the signal will be sent via a transducer mounted in the wet well. Sediment has not been considered in this change order. If sediment removal is required, it will be addressed via future change order.

We propose to perform the above work for the lump sum price of **\$ 53,700.00 (fifty-three thousand seven hundred dollars)** (please see attached breakdown for more information).

If acceptable, please issue a change order in the above amount and add ten (10) weeks to the contract time. This proposal only includes those items described above and included herein and doesn't include any unforeseen conditions. Due to unprecedented times and extreme material volatility, this change order proposal is good for fourteen (14) days and is subject to change after said date. We reserve the right to add additional costs for material price increases if incurred prior to approval/release. Please provide this change order as quickly as possible, so as not to delay the project.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION



Eric J. Andrew
Project Manager

EJA
cc: file
attach: Cost breakdown 04/29/21 (2 pgs)
Husker Power cut sheet (1pg)

CONTRACTOR'S LICENSE
WV 001651

P.O. BOX 247 • BRICKYARD ROAD
BUCKHANNON, WV 26201

PHONE (304) 472-3350
FAX (304) 472-8506

BRECKENRIDGE CORP.

BOWDEN FISH HATCHERY NEW RACEWAYS CONT 3 COP20

DATE 28-Apr-21

DESCRIPTION	EJA		WDMR BOWDEN FISH HATCHERY New Raceways COP20				SHT 1 OF 1	
	MAT'L	LABOR	EQUIP	SUB	TOTAL	COMMENTS		
COP 20 Flood Pump Engine Replacement	38,825	3,300	375	0	42,500			

SUBTOTAL 38,825 3,300 375 0 42,500

SUBTOTAL 0 0 0 0 0

SUBTOTAL 38,825 3,300 375 0 42,500

SUBTOTAL 2,330 1,056 2,330

SUBTOTAL 41,155 4,356 375 0 45,886

SUBTOTAL 218 218

SUBTOTAL 48,103 48,103

SUBTOTAL 63 63

SUBTOTAL 48,167 48,167

SUBTOTAL 531 531

SUBTOTAL 48,698 48,698

SUBTOTAL 0 0

SUBTOTAL 48,698 48,698

SUBTOTAL 7,005 7,005

SUBTOTAL 53,702 53,702

SUBTOTAL 0 0

SUBTOTAL 53,702 53,702

BID TOTAL 53,700 53,700

29-Apr-21

8:45

SHEET NO. 1

BRECKENRIDGE

May 18, 2021

Via email

Chapman Technical Group
P.O. Box 1355
200 Sixth Avenue
St. Albans, WV 25177

Att: Mr. Joe Bird, PLA, ASLA
Re: WVDNR Bowden Fish Hatchery Improvements Contract 3
Change Order Proposal # 21 Add Slide Gate at Effluent Box

Dear Mr. Bird,

As per your request, we are pleased to provide the following change order proposal to replace the 36" tide flex check valve in the existing effluent box with a 304 stainless steel slide gate for 36" ductile iron pipe (cut flush to wall) with manual rising stem bevel gear operator with hand crank (see attached cut sheet)

We propose to perform the above work for the lump sum price of **\$33,100.00 (thirty three thousand one hundred dollars)** (please see attached breakdown for more information).

As an alternate to the above, we can replace the 36" tide flex check valve in the existing effluent box with a 304 stainless steel flap gate for 36" ductile iron pipe (cut flush to wall) with double pin hinges and lifting eye (see attached cut sheet)

We propose to perform the above alternate work for the same lump sum price of **\$33,100.00 (thirty three thousand one hundred dollars)**

If acceptable, please issue a change order in the above amount (advising on the style gate you want) and add twelve (12) weeks to the contract time for procurement and installation. This proposal only includes those items described above and included herein and doesn't include any unforeseen conditions. Due to unprecedented times and extreme material volatility, this change order proposal is good for fourteen (14) days and is subject to change after said date. We reserve the right to add additional costs for material price increases if incurred prior to approval/release. Please provide this change order as quickly as possible, so as not to delay the project.

Please call if you have any questions or need any additional information.

Sincerely,
BRECKENRIDGE CORPORATION


Keith L. Skelton
Project Manager

EJA
cc: file
attach: Cost breakdown 05/18/21 (2 pgs)

Slide Gate cut sheet (1pg)

Flap Gate cut sheet (1pg)


CONTRACTOR'S LICENSE
WV 001631

P.O. BOX 247 • BRICKYARD ROAD
BUCKHANNON, WV 26201


PHONE (304) 472-3350
FAX (304) 472-8506

WACO Series 7674/6 Slide Gates


See Operators
Options page

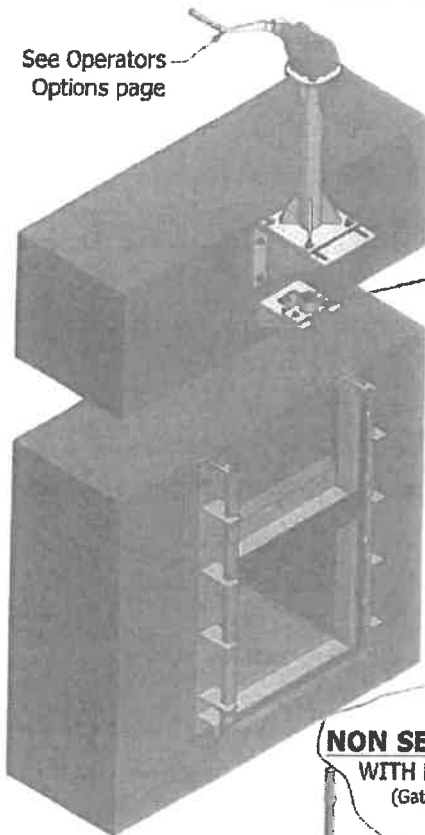

Stem guides
as needed

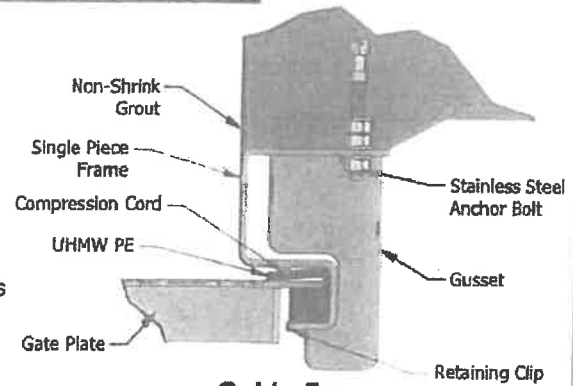



Guide Frame

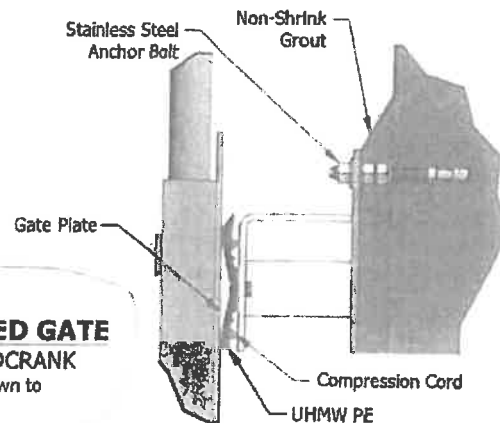

Upper Seal Frame

NON SELF-CONTAINED GATE
WITH BS2000 AND HANDCRANK
(Gate plate & stem not shown to
illustrate upper seal)

See Operator
Options page

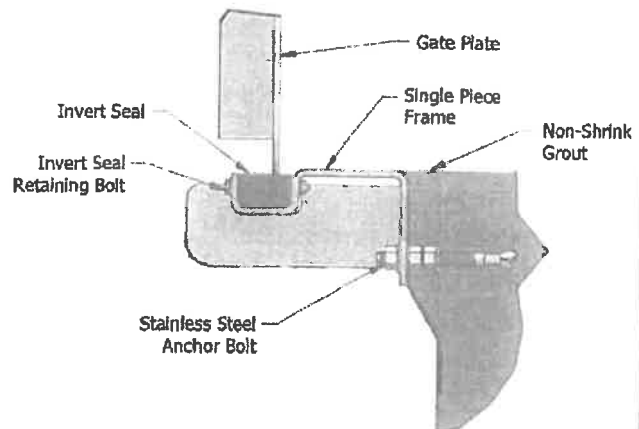
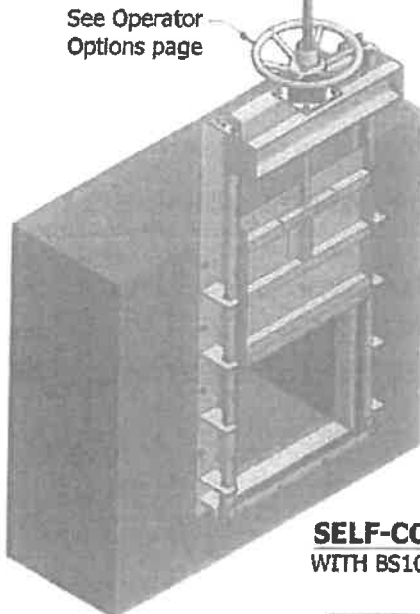


Invert Frame


SELF-CONTAINED GATE
WITH BS1015 AND HANDWHEEL

www.wacoproducts.com


WACO Series 3000 Flap Gate

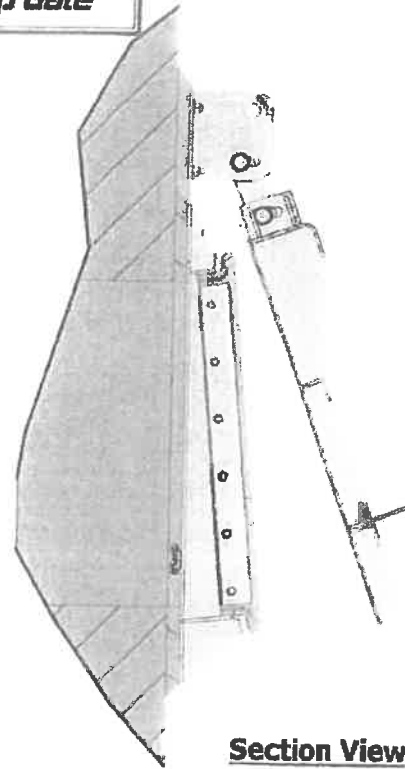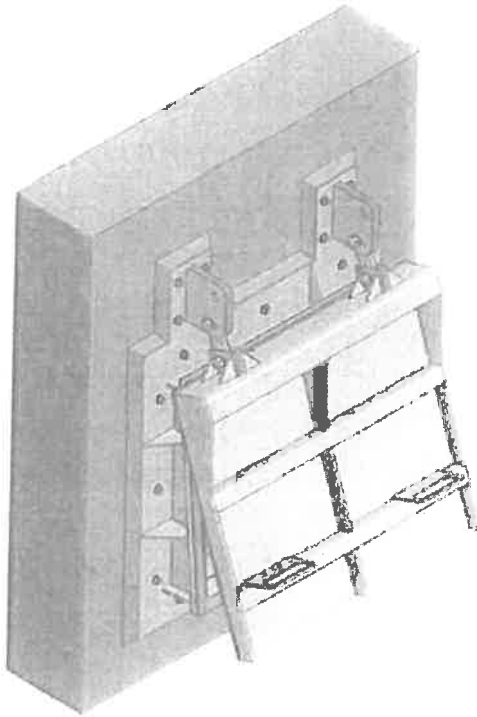

Section View

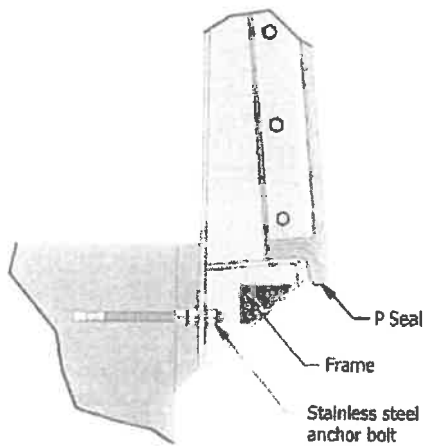

Invert Seal

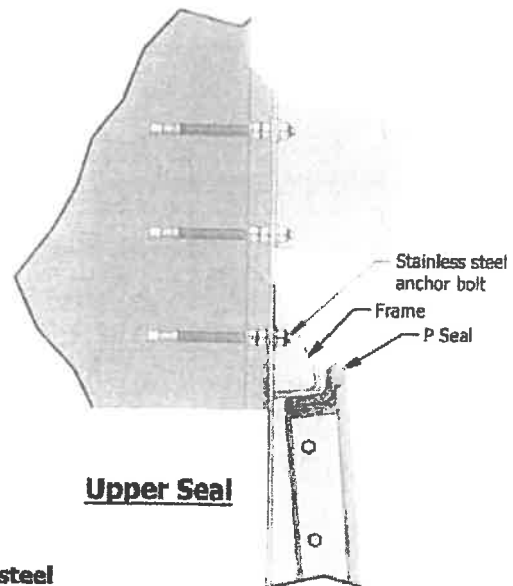

Upper Seal

NOTE: Flap gate frames can be aluminum or stainless steel and flaps can be aluminum, stainless steel, or rubber. Also available in square, rectangular, and round opening configurations. Frame can be gasket back and mounted directly to wall or pipe flange.

www.wacoproducts.com

WVDNR BOWDEN FISH HATCHERY New Raceways Cont 3 COP21						9HT 1 OF 1
	k/l's	DESCRIPTION	JOB TOTALS		TOTAL	COMMENTS
			MAT'L	LABOR	EQUIP	SUB
COP 21 Add Slide Gate @ off box			18,212	5,630	1,050	0
						24,892

DESCRIPTION	UNIT PRICE	QUANTITY	TOTAL	PERCENTAGE	TOTAL
LABOR ESCALATION	0.00	18,212	5,630	1.050	24,892
MATERIAL ESCALATION	0.00	0	0	0	0
SUBTOTAL		18,212	5,630	1.050	24,892
SALES TAX ON MATERIALS	6.1%	1,093	1,802	1.083	1,083
LABOR BURDEN	32%	19,305	7,432	1.050	27,786
SUBTOTAL		19,305	7,432	1.050	27,786
PD & PL INSURANCE					448
SUBTOTAL					28,232
BUILDERS' RISK INSURANCE					229
SUBTOTAL					28,461
PERFORMANCE BOND					327
SUBTOTAL					28,788
B&O TAX	0%				0
SUBTOTAL					28,788
OVERHEAD & ADMINISTRATIVE	15%				4,318
SUBTOTAL					33,107
MARKUP	0%				0
SUBTOTAL					33,107
BID TOTAL					33,100

BOWDEN FISH HATCHERY NEW RACEWAYS CONT 3 COP21

DATE 18-May-21

18-May-21

STATE OF WEST VIRGINIA
Purchasing Division

PURCHASING AFFIDAVIT

CONSTRUCTION CONTRACTS: Under W. Va. Code § 5-22-1(i), the contracting public entity shall not award a construction contract to any bidder that is known to be in default on any monetary obligation owed to the state or a political subdivision of the state, including, but not limited to, obligations related to payroll taxes, property taxes, sales and use taxes, fire service fees, or other fines or fees.

ALL CONTRACTS: Under W. Va. Code §5A-3-10a, no contract or renewal of any contract may be awarded by the state or any of its political subdivisions to any vendor or prospective vendor when the vendor or prospective vendor or a related party to the vendor or prospective vendor is a debtor and: (1) the debt owed is an amount greater than one thousand dollars in the aggregate; or (2) the debtor is in employer default.

EXCEPTION: The prohibition listed above does not apply where a vendor has contested any tax administered pursuant to chapter eleven of the W. Va. Code, workers' compensation premium, permit fee or environmental fee or assessment and the matter has not become final or where the vendor has entered into a payment plan or agreement and the vendor is not in default of any of the provisions of such plan or agreement.

DEFINITIONS:

"Debt" means any assessment, premium, penalty, fine, tax or other amount of money owed to the state or any of its political subdivisions because of a judgment, fine, permit violation, license assessment, defaulted workers' compensation premium, penalty or other assessment presently delinquent or due and required to be paid to the state or any of its political subdivisions, including any interest or additional penalties accrued thereon.

"Employer default" means having an outstanding balance or liability to the old fund or to the uninsured employers' fund or being in policy default, as defined in W. Va. Code § 23-2c-2, failure to maintain mandatory workers' compensation coverage, or failure to fully meet its obligations as a workers' compensation self-insured employer. An employer is not in employer default if it has entered into a repayment agreement with the Insurance Commissioner and remains in compliance with the obligations under the repayment agreement.

"Related party" means a party, whether an individual, corporation, partnership, association, limited liability company or any other form or business association or other entity whatsoever, related to any vendor by blood, marriage, ownership or contract through which the party has a relationship of ownership or other interest with the vendor so that the party will actually or by effect receive or control a portion of the benefit, profit or other consideration from performance of a vendor contract with the party receiving an amount that meets or exceeds five percent of the total contract amount.

AFFIRMATION: By signing this form, the vendor's authorized signer affirms and acknowledges under penalty of law for false swearing (W. Va. Code §61-5-3) that: (1) for construction contracts, the vendor is not in default on any monetary obligation owed to the state or a political subdivision of the state, and (2) for all other contracts, that neither vendor nor any related party owe a debt as defined above and that neither vendor nor any related party are in employer default as defined above, unless the debt or employer default is permitted under the exception above.

WITNESS THE FOLLOWING SIGNATURE:

Vendor's Name: Breckenridge Corp

Authorized Signature: _____

Date: May 20, 2021


State of West Virginia

County of Upshur, to-wit:

Taken, subscribed, and sworn to before me this 20 day of May, 2021.

My Commission expires April 11, 2026.

AFFIX SEAL HERE



NOTARY PUBLIC

Carey A. Wagner

Purchasing Affidavit (Revised 01/19/2018)

You are viewing this page over a secure connection. [Click here](#) for more information.

West Virginia Secretary of State — Online Data Services

Business and Licensing

Online Data Services Help

Business Organization Detail

NOTICE: The West Virginia Secretary of State's Office makes every reasonable effort to ensure the accuracy of information. However, we make no representation or warranty as to the correctness or completeness of the information. If information is missing from this page, it is not in the The West Virginia Secretary of State's database.

BRECKENRIDGE CORPORATION

Organization Information								
Org Type	Effective Date	Established Date	Filing Date	Charter	Class	Sec Type	Termination Date	Termination Reason
C Corporation	10/11/1984		10/11/1984	Domestic	Profit	BT		

Organization Information			
Business Purpose	2362 - Construction - Construction of Buildings - Nonresidential Building Construction (industrial, commercial & institutional building)		Capital Stock 1000000.0000
Charter County	Upshur	Control Number	0
Charter State	WV	Excess Acres	0
At Will Term	Member Managed		
At Will Term Years	Par Value		1.000000
1000000		Not Specified	

Authorized Shares	Young Entrepreneur

Addresses	
Type	Address
Local Office Address	1 BRICKYARD RD BUCKHANNON, WV, 26201
Mailing Address	PO BOX 247 BUCKHANNON, WV, 26201 USA
Notice of Process Address	PETER CASELLA PO BOX 247 BUCKHANNON, WV, 26201
Principal Office Address	BRICKYARD RD. BUCKHANNON, WV, 26201 USA
Type	Address

Officers	
Type	Name/Address
President	PETER J. CASELLA P.O. BOX 247 BUCKHANNON, WV, 26201
Secretary	CHRISTOPHER CASELLA P O BOX 247 BUCKHANNON, WV, 26201
Treasurer	CHRISTOPHER CASELLA P O BOX 247 BUCKHANNON, WV, 26201
Vice-President	ANTHONY CASELLA P O BOX 247 BUCKHANNON, WV, 26201
Type	Name/Address

Date	Amendment
8/8/1985	MERGER; MERGING UNIVERSAL COAL CORPORATION WITH

	AND INTO BRECKENRIDGE CORPORATION.
10/11/1984	CHANGE OF NAME FROM; CASELLA CONSTRUCTION COMPANY, INC.
11/30/1983	INCREASE; TO 1,000,000 AT 1,000,000 SHARES OF A PAR VALUE OF 1.00 EACH.
Date	Amendment

Annual Reports
Filed For
2021
2020
2019
2018
2017x
2017
2016
2015
2014
2013
2012
2011
2010
2009
2008
2007
2005
2004
2003
2002
2001
2000
1999
1998
