



2019 Washington Street, East Charleston, WV 25305 Telephone: 304-558-2306 General Fax: 304-558-6026

Bid Fax: 304-558-3970

The following documentation is an electronically-submitted vendor response to an advertised solicitation from the *West Virginia Purchasing Bulletin* within the Vendor Self-Service portal at *wvOASIS.gov*. As part of the State of West Virginia's procurement process, and to maintain the transparency of the bid-opening process, this documentation submitted online is publicly posted by the West Virginia Purchasing Division at *WVPurchasing.gov* with any other vendor responses to this solicitation submitted to the Purchasing Division in hard copy format.

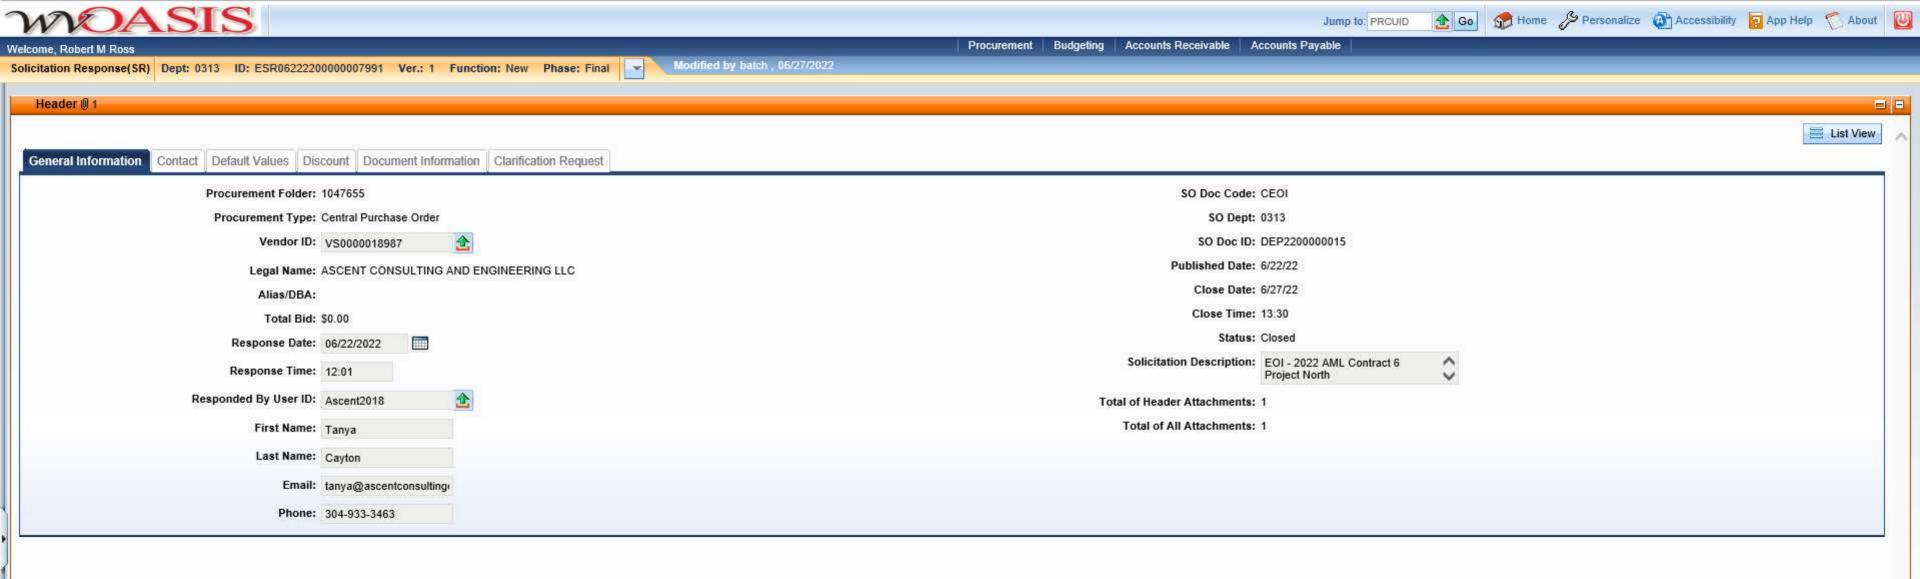



State of West Virginia Solicitation Response

Proc Folder: 1047655

Solicitation Description: EOI - 2022 AML Contract 6 Project North

Proc Type: Central Purchase Order

 Solicitation Closes
 Solicitation Response
 Version

 2022-06-27 13:30
 SR 0313 ESR06222200000007991
 1

VENDOR

VS0000018987

ASCENT CONSULTING AND ENGINEERING LLC

Solicitation Number: CEOI 0313 DEP2200000015

Total Bid: 0 Response Date: 2022-06-22 Response Time: 12:01:59

Comments:

FOR INFORMATION CONTACT THE BUYER

Joseph E Hager III (304) 558-2306 joseph.e.hageriii@wv.gov

Vendor Signature X

FEIN# DATE

All offers subject to all terms and conditions contained in this solicitation

Date Printed: Jun 27, 2022 Page: 1 FORM ID: WV-PRC-SR-001 2020/05

Line	Comm Ln Desc	Qty	Unit Issue	Unit Price	Ln Total Or Contract Amount
1	Professional Svcs - Clarksburg Post Landslide)			0.00

Comm Code	Manufacturer	Specification	Model #	
81100000				

Commodity Line Comments:

Extended Description:

Professional Svcs - Clarksburg Post Landslide

Line	Comm Ln Desc	Qty	Unit Issue	Unit Price	Ln Total Or Contract Amount
2	Professional Svcs - Fairmont Gateway Connector Portals				0.00

Comm Code	Manufacturer	Specification	Model #	
81100000				

Commodity Line Comments:

Extended Description:

Professional Svcs - Fairmont Gateway Connector Portals

Line	Comm Ln Desc	Qty	Unit Issue	Unit Price	Ln Total Or Contract Amount
3	Professional Svcs - Horners Run Portals				0.00

Comm Code	Manufacturer	Specification	Model #	
81100000				

Commodity Line Comments:

Extended Description:

Professional Svcs - Horners Run Portals

Line	Comm Ln Desc	Qty	Unit Issue	Unit Price	Ln Total Or Contract Amount
4	Professional Svcs - Lick Run 5				0.00

Comm Code	Manufacturer	Specification	Model #	
81100000				

Commodity Line Comments:

Extended Description:

Professional Svcs - Lick Run 5

Date Printed: Jun 27, 2022 Page: 2 FORM ID: WV-PRC-SR-001 2020/05



CEOI 0313 DEP2200000015

EOI-2022 AML Contract 6 Project North

DATE: June 22, 2022

SUBMITTED BY:

Ascent Consulting and Engineering LLC

Point of Contact: Jeff Knepper

2361 Davisson Run Road, Suite 103, Clarksburg, WV 26301

Tel: 304-933-3463

E-mail: jeffk@ascentconsultingengineers.com

Business Size Standard: Small Business

DUNS No: 067289907 CAGE Code: 8NJW5



Proprietary Statement

The information specifically identified on all pages of this sources sought response constitutes trade secrets or confidential commercial and financial information which Ascent believes to be exempt from disclosure under the Freedom of Information Act. Ascent requests that this information not be disclosed to the public, except as may be required by law. Ascent also requests that this information not be used in whole or part by the government for any purpose other than to evaluate the proposal, except that if a contract is awarded to Ascent as a result of or in connection with the submission of a proposal, the Government shall have the right to use the information to the extent provided in the contract.



TABLE OF CONTENTS

1	EXPR	ESSION OF INTEREST (EOI)	1.
2	EXPE	RIENCE – PROJECT SUMMARY INSERTS	2.
3	OUTL	INE	3.
	3.1	Key Personnel	3.
	3.2	Sub-Contactors	4.
	3.3	Project Methodology	4.
4	ATTA	CHMENT A – CQQ	
5	ATTA	CHMENT B – AML & RELATED PROJECT EXPERIENCE MATRIX (RPEM)	
6	ATTA	CHMENT C – RESUMES	
6	ATTA	CHMENT D – PROJECT TEAM	
7	ATTA	CHMENT E – CERTIFICATIONS/LICENSE	
		.CHMENT F – REQUIRED FORMS	



1 EXPRESSION OF INTEREST

Ascent Consulting and Engineering, LLC (Ascent) presents this centralized expression of interest (CEOI) to participate in this project released by the **WVDEP Office of Abandoned Mine Lands and Reclamation** (**WVDEP-DLR-AML**). Ascent is prepared to meet the **WVDEP's** expectations sited within the original CEOI to provide the following engineering design services for Contract 6 – West Virginia North Projects (Clarksburg Landslide, Fairmont Gateway Connector Portals, Horners Run Portals, Lick Run 5):

- NEPA consultation and documentation
- Public Participation
- Infrastructure Investment Job Act (IIJA) compliance
- Determine legal ownership of properties
- Obtain exploratory and construction rights of entry
- Provide legal documentation to justify legal ownership findings
- Provide current mapping, perform survey and other related services
- Perform site and geotechnical investigations
- Design temporary and permanent access or accesses for construction and future maintenance
- Design and stabilize landslides
- Design multiple portal seals and regrades
- Design and mitigate AMD Drainage, including possible horizontal borings
- Design reclamation of exposed coal refuse and mine spoil
- Design drainage conveyances, including drainage channels underdrains, and/or other controls to safely convey water off-site
- Design to demolish/dismantle and remove concrete silo
- Design to demolish waste structures and derelict equipment
- Condition and revegetate all disturbed areas
- Construction quality assurance and quality control (QA/QC)
- Provide resident project representative/inspector
- Prepare daily construction activity logs summarizing activities
- Provide engineering support and services throughout construction
- Provide Engineers certification report

We acknowledge the importance of this opportunity and commit our experience and cooperation as outlined in the sections below:

- Experience Listing of Projects
- Outline (resources, sub-contractors, and key personnel)

Ascent Consulting and Engineering, LLC (Ascent) is a Small Business headquartered in Clarksburg, West Virginia. Collectively, our management team has over **50 years** of related experience. Ascent is equipped with a team of professionals, who are experts in their fields and have a comprehensive understanding of construction, engineering, environmental, and best management practices. Ascent has built a network of reliable subcontractors and will pull out all stops for the successful completion of this project! Ascent also maintains an AASHTO accredited materials testing laboratory and provides construction management and inspection services. **A true full-service firm!**

The **Ascent Team** stands out because of our core competencies that match the requirements of this solicitation:



- Experience working highly complex engineering design services projects.
- Fully licensed and insured.
- Direct AML project experience and strong references.
- Substantial experience with managing various of projects and task orders simultaneously.
- An intimate understanding of state and federal standards for safety, and quality.
- Ability to determine the most efficient and cost-effective solutions that meet project goals.
- The Ascent Team has significant project experience in over 15 states.
- The Ascent Team can quickly respond to any Task Order that may be issued through this contract, wherever services are needed.

Ascent sincerely thanks the **WV Purchasing Division and the WVDEP-DLR-AML** for this unique and exciting opportunity. We greatly appreciate the opportunity to showcase our Team.

2 EXPERIENCE - PROJECT LISTING INSERTS

GLOBE MINE



SCOPE INCLUDES:

- Water Quality Assessment
- NPDES Compliance
- Acid Mine Drainage
 Remediation
- Geotechnical Investigation
- Drainage Conveyance

CHALLENGE


Water from 789 Globe Mine which is an old clay mine in Newell, WV was causing contamination to surface water streams. The iron rich water was causing water quality concerns to nearby industrial facilities and eventually to the Ohio River. The existing treatment system failed and the quantity of water from the mine rose exponentially.

SOLUTION

Ascent was tasked with developing a new system to treat the acid mine drainage as well as handle to increased quantity of mine water. A break-wall was installed in the first mine opening to act as a secondary containment to facilitate a steady flow rate. The mine water was pumped to a main aeration pond to facilitate iron sediment settlement. A series of ponds were modified to filter the heavy metals so the water could then be discharged to an onsite stream. With little area to work in Ascent designed a treatment system to handle the increased mine water volume and maintain compliance with the NPDES permit requirements. Extensive hydrogeologic and geotechnical investigations were conducted to determine the mine water pathways and the underground mine workings.

BENEFIT

By modifying the treatment system to handle the increased mine water compliance with the NPDES permit was achieved. Mine seepage and contamination no longer affected nearby industrial facilities or seeped to the Ohio River.

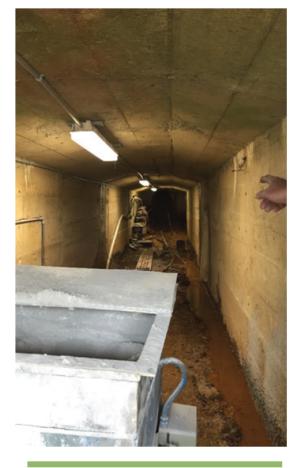

- PROJECT MANAGER: JEFFREY KNEPPER
- CLIENT: VESUVIUS
- PROJECT LOCATION: NEWELL, WV
- PROJECT STATUS: COMPLETED
- PROJECT COST: \$2.5 MILLION

LEON STREET SLIP REPAIR



CHALLENGE

A slip occurred in the Town of Clarksburg, WV likely caused by slope instability. Ascent was contracted to investigate the slip and complete an engineering design to mitigate the hazard. The location of the slip affects a residence above and commercial businesses below.

SOLUTION

Ascent facilitated three test borings to evaluate the soil characteristics and subsurface structures at the slip location. The borings would help determine the cause of the slip and potential solutions. Upon further investigation the slope instability was the result of a collapsed room and pillar abandoned mine. Based on this information the engineers determined the mine void would be filled and sealed and an H-Pile Retaining Wall would be stalled to mitigate slope stability. Funding was provided via the West Virginia Environmental of Protection (WVDEP) Abandoned Land Mines (AML) Program. Total cost of project: \$1,200,000.

BENEFIT

By finding the root cause of the slope stability the hazard was mitigated to the satisfaction of the WVDEP, the residence, and the commercial businesses on time and within a set budget.

SCOPE INCLUDES:

- Survey and Mapping Services
- Geotechnical Evaluation
- Engineering
- design/specifications
- Environmental Assessment/NEPA
- Construction Pre-Bid Documents
- Construction Inspection



- PROJECT MANAGER: MIKE NESTOR
- CLIENT: TOWN OF CLARKSBURG
- PROJECT LOCATION: HARRISON COUNTY, WV
- PROJECT STATUS: ACTIVE
- PROJECT COST: \$1.2 MILLION

ROARING CREEK



CHALLENGE

Abandoned mines and karst terrain was causing a loss of water from ponds located at a farm in Coalton, WV. The old mines and sinkhole instability were causing mine seepage to other parts of the farm.

SOLUTION

An extensive geotechnical investigation was conducted to map the various conduits of the mine portals and the hydrogeologic connections to the sinkholes. Once identified a wet mine seal design was developed. Based on the geotechnical grid the mine portals were spread across the vast terrain of the farm. The sinkholes and mine collapses were characterized, and measures were taken to stabilize them across the project area. The farm ponds were losing water and mine seepage was percolating back into the ponds. Regrading was performed around the pertinent site features to work around sinks, ensuring runoff would continue to the feed pond.

BENEFIT

The issues from the abandoned mines and the karst terrain allowed the farm to stabilize. The loss of pond water was corrected so water was retained, and mine seepage was directed elsewhere. The remediation and modifications were performed within on time and within a set budget.

SCOPE INCLUDES:

- Geotechnical Evaluation
- Piezometer Installation
- · Wet Mine Seal Design
- Karst Terrain/Sinkhole
 Stabilization
- Acid Mine Drainage Remediation
- Drainage Conveyance



- PROJECT MANAGER: MIKE NESTOR
- CLIENT: PRIVATE
- PROJECT LOCATION: COALTON, WV
- PROJECT STATUS: COMPLETED
- PROJECT COST: \$2 MILLION

THE SHILOH DEVELOPMENT



CHALLENGE

The Shiloh Development is approximately 100 acres of land off I-79 near Stonewood, WV. The initial investigation revealed an abandoned coal mine that required a geotechnical to determine the best remedial option for stability and remediation. Stream and wetland, cultural a habitat studies were also a part of this development.

SOLUTION

Ascent was tasked with investigating the characteristics of the existing abandoned coal mine. A geotechnical investigation was initiated to determine the extent and stability of the mine. These results are crucial to the civil design concept and site development. A stream and wetland delineation of the 100-acre property was suggested as well as a cultural resources and habitat survey. These studies are vital to understanding the property and what state and federal environmental permitting is required. The project has received \$5 million from the WVDEP AML Program.

BENEFIT

Understanding and characterizing the existence of the old coal mine helps correctly design necessary stability components within the full development of the site. It also adds an additional funding source in State and Federal Grant money for project completion.

SCOPE INCLUDES:

- Survey and Mapping
 Services
- Geotechnical Evaluation
- Engineering Concept
 Design
- Stream and Wetland
 Delineation
- Cultural Resources Survey
- Water Quality Assessment



- PROJECT MANAGER: MIKE NESTOR
- CLIENT: PRIVATE
- PROJECT LOCATION: HARRISON COUNTY, WV
- PROJECT STATUS: ACTIVE
- PROJECT COST: \$25 MILLION

ANGLINS



SCOPE INCLUDES:

- Geotechnical Evaluation
- Piezometer Installation

Wet Mine Seal Design

- Environmental Assessment
- Drainage Conveyance
- Construction Inspection

CHALLENGE

Mine seepage was identified and flowing freely from the hillside near Anglins Run. The seepage was causing stability issues with a nearby parking lot. As this poses an environmental threat a further investigation as to the cause and nature of the mine seepage.

SOLUTION

A Piezometers were installed to identify pavement and wall elevations to determine the source of the mine seepage. A geotechnical evaluation was conducted to investigate the extent of mine workings and portals. A wet mine seal design was implemented to mitigate the portals. Conveyance ditching was designed with noncalcareous stone and regraded to provide proper drainage and stabilize the parking lot. Funding was provided via the West Virginia Department of Environmental Protection (WVDEP) Abandoned Land Mines (AML) Program. Total cost of project: \$475,000.

BENEFIT

The issues from the abandoned mines and the karst terrain allowed the farm to stabilize. The loss of pond water was corrected so water was retained, and mine seepage was directed elsewhere. The remediation and modifications were performed within on time and within a set budget.

- PROJECT MANAGER: MIKE NESTOR
- CLIENT: WVDEP-AML:
- PROJECT LOCATION: PHILIPPI. WV
- PROJECT STATUS: COMPLETED
- PROJECT COST: \$ 450,000



3 OUTLINE

People and processes are important resources needed for the WVDEP. The section below defines Ascent's resources, subcontractors, and key personnel.

3.1 KEY PERSONNEL

Leadership and staffing are the most important quality of Ascent. Ascent's strategy and competitive advantage is founded on providing the most professional, technically competent, and highly trained leaders for each client. The table below lists the Ascent Key Personnel and their skills.

Michael Nestor, PE Managing Member	Mr. Nestor is the founder and Managing Member of Ascent Consulting and Engineering. He has over 18 years of engineering and consulting experience and previously served as the "Site Division Manager" for a larger, regional engineering firm. Mike will function as the Team Lead for this project, providing experience, communication, and QA/QC. Mike provides site development and re-use planning experience.
Jeffrey A. Parobek, PE Project Engineer	Mr. Parobek will be the Project Engineer. Mr. Parobek has 40 years' experience and maintains a B.S. in Mining Engineering along with a P.E. in Civil Engineering. He is responsible for the overview of technical aspects of project design, design coordination with clients and other members of the design team, public presentations of projects in front of governing bodies, regulatory agencies and at stakeholder meetings, coordination of project bid process and oversight of services during construction including change order and pay application reviews, coordination with other managers for manpower and scheduling, preparation of price proposals and statements of qualifications, preparation of invoices and supplemental work requests.
Jeff Knepper, CPG, LRS Senior Environmental Manager	Mr. Jeff Knepper will be the Licensed Remediation Specialist for this AML Project. Mr. Jeff Knepper is a senior environmental manager and former program manager for the West Virginia Department of Environmental Protection with over 24 years of experience. He worked with the Division of Water and Waste Management to review, develop and approve groundwater protection and remediation plans. He has worked closely with the WV Voluntary Remediation Program (VRP) and spent significant time negotiating as a regulator and consultant for remedial activities for the WVDEP and the EPA. He is a certified Professional Geologist and a West Virginia Licensed Remediation Specialist. Jeff will provide environmental support and leadership for this project.
Amanda Wright Environmental Manager	Amanda will be a subject matter expert while providing overall project management and guidance. Amanda Wright has over 18 years' experience managing large scale and complex environmental projects throughout WV, OH, & PA.



Megan Wagner Environmental Scientist	Megan is a certified wetland specialist with certifications from the USACE among others. She has over 7 years' experience in stream and wetland delineations, soil assessments, GIS mapping and data processing. Megan is also a Certified Asbestos Inspector.
Sara Hltaky Staff Scientist	Sara has over 4 years of experience with data collection, plan writing and mapping for a variety of earth disturbance and agriculture projects. Her experience also includes stream assessments and monitoring. Sara is also a Certified Asbestos Inspector.

3.2 SUB-CONCONTRACTORS

Ascent Consulting and Engineering has formed a team of subcontractors, listed in the table below, who bring experience to cover all tasking for the WVDEP.

Geotechnical Partner:

ECS MID-ATLANTIC, LLC

www.ecslimited.com



3.3 PROJECT METHODOLOGY

Ascent strongly believes that clear communication and expectations are at the core of every successful project. We will encourage a kickoff meeting with your staff and our design team at the onset of the project for discussion about existing conditions, project goals, availability of funds, site operations, and perceived challenges, etc. This meeting allows us to fully understand the project and to tailor our approach and communication to that of your liking. It is our goal to support the overall vision by providing our experienced team to offer valuable suggestions, looking for efficient ways to accomplish the project goals, and executing a plan that is easily understood, constructed, and ultimately fixes the problem.

At a minimum, Ascent facilitates projects according to the following procedure:

Project Kickoff Meeting

- Sets expectations for scope, budget, schedule, communication procedure, etc.
- Informs team with respect to subconsultants and other outside factors.
- Review of site history and preferred plan.
- Discuss preferences and limitations to site access and other important items.
- Develops "action items" and delivery dates based on various decision points.



Environmental Considerations

- Environmental assessments and reports will be prepared and submitted based on the project parameters.
- Reports/Assessments may include NEPA, characterization reports, treatment/mitigation studies,
 AMD treatment alternatives and design. Other reports or investigations may be prepared based on the requested agency.

Conceptual Layout and Preliminary Cost Estimation

- On a conceptual level, Ascent will prepare recommendations for project implementation along with preliminary construction cost estimates and input on what each alternative will improve for overall drainage. The intent of this phase is to find the "most bang for your buck".
- After the concepts have been presented to and discussed with the stakeholders, Ascent will move forward with the design of the preferred alternative(s).
- During this process, various items are completed concurrently such as base mapping, ground survey, geotechnical evaluations, and the ultimate maintenance of the site. Any site work such as clearing and grubbing or minor grading for rig access should be coordinated with the proposed plan in order minimize rework and help to hold down project costs.
- This stage allows the project team to refine the concept and identify anything initially unforeseen that would have an impact to project cost or constructability.
- Permit requirements will be evaluated and drafted during this phase.

Plan Production

- After budgets, feasibility, land acquisitions, etc. are confirmed, Ascent will begin assembling plans and specifications for construction as well as permit submittals.
- The Ascent Project Manager will provide a weekly email update to the WVDEP outlining work completed, the schedule ahead, and any changes. Significant changes or new information found that is anticipated to require project adjustments will be brought to the WVDEP immediately. Initial contact in this instance is always a phone call, followed by a recap email and in some cases, face to face meetings if representatives are available. Project budgets and schedules are reevaluated at milestones (typically at 30%, 60%, and 90% completion).
- The keys to project success for this site include but are not limited to site investigation, removal of existing treatment systems, conveyance and mitigation of AMD drainage, conveyance of site runoff and impounded water, re-grading of the project area, and revegetation of all disturbed areas.
 - The existing treatment systems will be modified or removed based on design specifications. The level of modification will be determined based on the initial site investigation.
 - AMD will need to be relieved; they will focus on the design of the drainage conveyances as well as mitigation strategies. It will be important to plan not only for the final conditions but also for construction activities and grading operations that may need to be staged to prepare for possible release of water during construction activities.
- Finally, the design will be evaluated for long term sustainability to reduce or completely eliminate maintenance after construction is complete. The plan will be devised in a way that fixes the problem at hand yet minimizes disturbance to the existing landscape. We understand that



vegetation is an important factor to stabilization so any areas that can remain undisturbed will be exonerated from clearing and grubbing activities. In addition, areas that require clear cut will be planned for revegetation to re-stabilize the surface as quickly as possible. The team assembled for this project has extensive experience in geotechnical exploration and design, landslide remediation, hydrology/hydraulics, drainage design, permitting, and AMD treatment processes as well as many other relevant project tasks.

Construction Management and Project Inspection

The project manager in charge will also serve as the Project Manager throughout construction. He/She will help to identify the proper field personnel to inspect the project, will speak to the inspector daily, and will attend contractor/progress meetings throughout the duration of the project. He/She will review and submit daily reports to ownership and notify the Client immediately if any problems arise. The Project Manager will also review/approve pay applications submitted by the contractor.

Project Finalization

Ascent will constantly evaluate progress to ensure that the project is on schedule and that pay
applications are consistent with the work completed.

The primary objectives of the management framework / processes are:

- Time, Cost and Scope Cost, schedule, and quality control are key components of the Ascent Team's management approach. This module is primarily concerned with defining and controlling the project; tracking, modifying, and controlling the steps for realizing the anticipated project benefits; and providing a structure to manage change. We will use cost, schedule, and quality performance measures agreed to during the kickoff meeting to monitor progress.
- Communications and Reporting: Ascent understands communication is a key to success for this effort, and good communication will deliver key messages to stakeholders and other team members. This includes status of activities, schedule, and informational awareness on the project and/or task, as well as reporting on a weekly, monthly, or contract basis.
- Financials: Ascent utilizes resource planning, cost estimating based on effort, cost budgeting and cost control processes to ensure that the project is completed within the approved budget. Projects are tracked financially, and billing activities are monitored and controlled along with the collection processes.
- Quality Management: All studies for the project will be performed to the industry standard to adhere
 to proven guidelines. The reports that are generated are peer reviewed internally as a quality control
 measure.
- Resource Management: Our resource management approach ensures that pre-planning, scheduling, and the allocation of Ascent's resources will maximize efficiency for the Brownfield Environmental Assessment and Planning project.
- Change Management: Ascent's change management approach is to first stop and pause to understand what is driving the change. Once this is understood, it is communicated directly to the client so that a clear path forward can be developed.
- Knowledge Management: Our knowledge management process includes collecting, organizing, clarifying, and disseminating information and knowledge throughout an organization and our



- customers. Ascent has developed and maintains an in-house Sharepoint knowledge management site. This knowledge management site is used to house project specific documentation including workflows for routing and approvals.
- Risk / Issue Management: Our risk management approach is to reduce the variation in expected project results, including cost, schedule, and performance. Risk management begins with the development of our Risk Management Plan that will continue throughout the life of the project with active participation by all stakeholders. Our PM will manage the Risk Plan, which will contain a description of the risk, the risk category, the risk impact assessment, the risk ranking and urgency, the originator, and the name of the assigned manager/staff member. All problems and issues associated with project performance or related issues will be identified, qualified, and documented in the form of action items, assigned to a responsible individual, entered our Quality Control database, and tracked to resolution. We will employ our rapid issue escalation process via daily stand-up meetings and weekly status reports from our key personnel staff. The Project Manager will ensure that any adverse trends are analyzed for root causes and that appropriate corrective actions are taken.

ATTACHMENT A

V	VEST VIRGINIA DEPARTMEN	IT OF ENVIRONMENTAL E	PROTECTIO	ON
	AML CONSULTANT QUA	ALIFICATION QUESTION	NAIRE	Attachment "A"
PROJECT NAME AML 2022 Contract 6 - North	DATE (DAY, MONTE June 22, 2022	H, YEAR)	FEIN 82-406924	0
1. FIRM NAME Ascent Consulting and Engi LLC	neering, 2361 Davis	CE BUSINESS ADDRESS sson Run Rd Suite 103 g, WV 26301	3. FOR N/A	MER FIRM NAME
4. HOME OFFICE TELEPHONE (304) 933-3463	5. ESTABLISHED (YEAR) 2018	6. TYPE OWNERSHIP Individual Corpora ☑Partnership Joint		6a. WV REGISTERED DBE (Disadvantaged Business Enterprise) YES ☑NO
7. PRIMARY AML DESIGN OFFICE: 2361 Davisson Run Rd Suite 10				
8. NAMES OF PRINCIPAL OFFICER Michael R. Nestor, PE (Managi Zachary L. Assaro (Member)		8a. NAME, TITLE, & TELE	PHONE NUME	SER - OTHER PRINCIPALS
	- ECOLOGISTS - ECONOMISTS - ELECTRICAL ENGINEERS 3 ENVIRONMENTALISTS - ESTIMATORS 1 GEOLOGISTS - HISTORIANS 1 HYDROLOGISTS STERED PROFESSIONAL ENGINER and Mining must provide sugnitions type of work.		EERS RS REGIONAL RS	- STRUCTURAL ENGINEERS 6 SURVEYORS - TRAFFIC ENGINEERS - OTHER 42 TOTAL PERSONNELL ies them to
10. HAS THIS JOINT-VENTURE WC	ORKED TOGETHER BEFORE? N/A	□ YES □ NO		

Geotech	11. OUTSIDE KEY CONSULTANTS/SUB-CONSU	JLTANTS ANTICIPATED TO BE USED. Attach "AML	Consultant Qualification Questionnaire".
NAME AND ADDRESS: NAME AND ADDRESS: SPECIALTY: NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE	NAME AND ADDRESS:	SPECIALTY:	WORKED WITH BEFORE
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes		Geotech	
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes			<u> </u>
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes			No
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE	NAME AND ADDRESS:	SPECIAL TV:	
NAME AND ADDRESS: SPECIALTY: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE	NAME AND ADDRESS.	SILCIALI I.	WORKED WITH BEI ORE
NAME AND ADDRESS: SPECIALTY: SPECIALTY: WORKED WITH BEFORE Yes NO WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			Yes
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE	NAME AND ADDRESS:	SPECIALTY:	WORKED WITH BEFORE
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes			Voc
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			168
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			No
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE	NAME AND ADDRESS:	SPECIALTY:	
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			Yes
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE YesNo NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			No
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE	NAME AND ADDRESS:	SPECIALTY:	
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			Yes
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes NO NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE LYes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE LYes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE LYes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE	NAME AND ADDRESS.	CDECIAL TV.	
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE	NAME AND ADDRESS.	SPECIALIT.	WORKED WITH BEFORE
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NO NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			Yes
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE NO WORKED WITH BEFORE			
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE WORKED WITH BEFORE	NAME AND ADDRESS:	SPECIALTY:	WORKED WITH BEFORE
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			Vac
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE Yes No NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			105
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			No
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE	NAME AND ADDRESS:	SPECIALTY:	WORKED WITH BEFORE
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			Yes
NAME AND ADDRESS: SPECIALTY: WORKED WITH BEFORE			No
	NAME AND ADDRESS:	SPECIALTY:	
Yes			
			Yes
No			No

12.	Α.	Is your	firm's	personnel	experienced	in	Abandoned	Mine	Lands	Remediation/Mine	Reclamation	Engineering?
-----	----	---------	--------	-----------	-------------	----	-----------	------	-------	------------------	-------------	--------------

YES Description and Number of Projects: Performed design for various projects dealing with mine seepage and ground instability. Coordinated drilling/monitoring activities, designed wet mine seals, drainage conveyances, E&S measures, and slip repairs, etc. Approximately 13 projects completed. Specifically, Mr. Nestor was heavily involved in the Anglins Run and Roaring Creek projects as well as several others. Mr. Knepper has been involved with several AMD remediation active and passive treatment systems.

NC

B. Is your firm experienced in Soil Analysis?

Description and Number of Projects: Ascent staff is experienced with identifying hydric soils applicable to wetlands and subsequent permitting needs. Ascent is also experienced with reading boring logs and coordinating with Geotechnical Engineers in order to apply information to practical designs. Ascent personnel has provided such services on dozens of projects. Ascent's Environmental Division Manager is a Certified Professional Geologist.

NO

C. Is your firm experienced in hydrology and hydraulics?

YES Description and Number of Projects: <u>Ascent personnel performs pre and post watershed analyses on a variety of projects.</u> We have completed drainage studies for municipalities, private development projects, and AML projects. We have also performed stream analyses for bridge replacement projects and development in flood prone areas. This type of work is performed in nearly every project Ascent works on and has been completed in hundreds of projects.

NO

D. Does your firm produce its own Aerial Photography and Develop Contour Mapping?



Description and Number of Projects:

NO Ascent produces aerial photography and develops contour mapping in-house. Ascent recently formed a survey division which includes 6 in-house surveyors.

E. Is your firm experienced in domestic waterline design? (Include any experience your firm has in evaluation of aquifer degradation as a result of mining.)

YES Description and Number of Projects: Ascent is experienced with the design and layout of potable water systems for commercial and residential development projects. We have completed dozens of mainline extensions and/or replacement projects. Ascent's Environmental Manager does have experience with aquifer degradation as it relates to mining. He was previously and Environmental Resource Program Manager for the Division of Mining and Reclamation.

NO

F. Is your firm experienced in Acid Mine Drainage Evaluation and Abatement Design?

YES Description and Number of Projects: Ascent Personnel has developed several projects dealing with evaluation of Acid Mine Drainage and design of conveyance/treatment systems. Approximately 13 projects completed. In addition, Jeff Knepper (Ascent) has extensive experience in Acid Mine drainage treatment both on the consulting side as well as the Regulatory side. He was formerly an Environmental Resources Program Manager for the Department of Mining and Reclamation for the WVDEP.

NO

13. PERSONAL HISTORY STATEMENT OF PR	INCIPALS AND ASSOCIATES RESPO	NSIBLE FOR AML PROJECT DESIGN	(Furnish complete
data but keep to essentials)			
NAME & TITLE (Last, First, Middle Int.)		YEARS OF EXPERIENCE	
Nestor, Michael, R.	YEARS OF AML DESIGN EXPERIENCE: 15	YEARS OF AML RELATED DESIGN EXPERIENCE: 18	YEARS OF DOMESTIC WATERLINE DESIGN EXPERIENCE: 18
Brief Explanation of Responsibilitie	S		
Mr. Nestor has served in various rol Mr. Nestor worked as a staff enginee division for a large regional design Managing Member for the firm. He is review for projects. Mr. Nestor has transportation/access roads, landsli	r, project engineer, project of firm before starting Ascent of very heavily involved in all and continues to work with drawn	manager, and then led an entime Consulting and Engineering. He aspects of the firm's work inc	re site development e now serves as the cluding design and
EDUCATION (Degree, Year, Specializat Bachelor of Science in Engineering T			
MEMBERSHIP IN PROFESSIONAL ORGANIZAT American Society of Civil Engineers American Society of Highway Engineer Region)		REGISTRATION (Type, Year, Sta Professional Engineer, 2009, Professional Engineer, 2020, Professional Engineer, 2020, Professional Engineer, 2020,	WV PA VA
13. PERSONAL HISTORY STATEMENT OF PR data but keep to essentials)	INCIPALS AND ASSOCIATES RESPO		
NAME & TITLE (Last, First, Middle Int.) Assaro, Zachary, L.		YEARS OF EXPERIENCE	
2.	YEARS OF AML DESIGN EXPERIENCE: 7	YEARS OF AML RELATED DESIGN EXPERIENCE: 9	YEARS OF DOMESTIC WATERLINE DESIGN EXPERIENCE:9
Brief Explanation of Responsibilitie Mr. Assaro served as a staff enginee prior to joining Ascent Consulting a management work for a variety of promanagement, land development, public	r, project engineer, and then nd Engineering as a co-owner/pect types including but not	member. Mr. Assaro has perform limited to access roads, drain	med design and
EDUCATION (Degree, Year, Specializat Bachelor of Science in Engineering T			
MEMBERSHIP IN PROFESSIONAL ORGANIZAT	IONS	REGISTRATION (Type, Year, Sta	ate)

		<i>-</i>					
13. PERSONAL HISTORY STATEMENT OF Production data but keep to essentials)	RINCIPALS AND ASSOCIATES RESPO	NSIBLE FOR AML PROJECT DESIGN	(Furnish complete				
NAME & TITLE (Last, First, Middle Int.)		YEARS OF EXPERIENCE					
Short, Eric, M.	YEARS OF AML DESIGN EXPERIENCE:		YEARS OF DOMESTIC WATERLINE DESIGN EXPERIENCE:18				
Mr. Short has been involved in near for Ascent Consulting and Engineering	ly every facet of civil engine ng. Mr. Shorts experiences cov	vers large land development pro					
		. <u>C.</u>					
American Society of Civil Engineers		REGISTRATION (Type, Year, St. N/A	ate)				
NAME 6 TITLE (last, Pirst, Middle Int.) Short, Eric, M. WEARS OF AME. DESIGN EXPERIENCE: WEARS OF AME. RELATED DESIGN WIERER OF COMMETTED EXPERIENCE: SYERIENCE: SYERIENCE EDUCATION (Degree, Year, Specialization) Bachelor of science in Engineering Technology, 2003 MEMBERSHIP IN PROFESSIONAL ORGANIZATIONS American Society of Civil Engineers N/A MEMBERSHIP (Int., Pirst, Middle Int.) SYERIENCE: SYER							
NAME & TITLE (Last, First, Middle Int.)							
Knepper, Jeffrey			WATERLINE DESIGN				
		vever maintains a wide variety	of duties within the				
above ground storage tanks. Jeff propermitting and compliance approvals	eviously served as an Environm for mining facilities in the	mental Resources Program Managestate of WV. His background c	er for WVDEP, handing				
American Institute of Professional (West Virginia Manufacturers Associa GO WV	Geologists	Professional Geologist, VA Licensed Remediation Specialist, WV Certified Aboveground Storage Tank Inspector, STI-					

	PROVIDE A DESIGN SER		SOFTWARE	AND EQUIP	PMENT AVA	ILABLE II	N THE PR	IMARY O	FFICE W	WHICH WILL	BE USED T	O COMPLE	TE AML	
Auto	CAD Civil	. 3D (202	20), Micro	osoft Suit	ce, Vehic	le Track	ing, Hyd	raflow Z	Add on	from Auto	Desk, HEC	-RAS, Goo	ogle Earth,	
GPS	Pathfinder	Office	, Terrain	Navigator	r Pro, ARG	C GIS, A	dobe Acr	obat DC	, Sage	(Financia	l Software	:)		
														_
														_
														_
														_
														_
														_
														_
														_
														_
														_
														_

15. CURRENT ACTIVITIES	ON WHICH YOUR FIRM IS TH	E DESIGNATED ENGINEER OF	RECORD				
PROJECT NAME, TYPE AND LOCATION	NAME AND ADDRESS OF OWNER	NATURE OF YOUR FIRM'S RESPONSIBILITY	ESTIMATED CONSTRUCTION COST	PERCENT COMPLETE			
Cacapon Resort State Park I&I Study	WVDNR 324 4 Th Avenue South Charleston, WV 25303	Preliminary Engineering Study to determine needed system upgrades	Not yet determined	15% Design			
Realizations 789, AMD Treatment, Hancock County WV	Vesuvius 250 Parkwest drive Pittsburgh PA	Active and passive AMD treatment systems, Permitting, UIC.	\$1,500,000	100% Complete			
Lost Creek Natural Gas replacement, 8 mile replacement, Harrison County WV	Dominion Energy Transmission Southern Regional Headquarters, Weston, WV	Transmission Line design, environmental clearances & permitting, construction administration, survey, inspection	\$5,000,000	Design Complete/ Construction Starts Spring 2021			
Leon Street Slip, AML Grant, Clarksburg WV	Town of Clarksburg, WV	Hydrologic Analysis, Slip Repair, NEPA development, AML grant preparation	\$1,000,000	50% complete - Construction phase			
Yocum Slip Repair	Southwester Energy 1300 Fort Pierpont Dr Morgantown, WV 26508	Evaluate Existing slip in roadway, perform geotechnical investigation, and design slip repair plan	\$1,000,000	25% Design			
Lewis County Broadband	Lewis County Commission	110 Center Avenue Weston, WV 26452	\$500,000	2%			
Gnats Run Road Slip	Antero Resources White Oaks Blvd. Bridgeport, WV	Geotechnical Evaluation, slip repair design	\$250,000	95% Design			
TOTAL NUMBER OF PROJECT	S:7	TOTAL ESTIM	ATED CONSTRUCTION COSTS:	\$8,250,000			

PROJECT NAME, TYPE AND LOCATION	NATURE OF FIRMS RESPONSIBILITY	NAME AND ADDRESS OF OWNER	ESTIMATED COMPLETION DATE	ESTIMATED CONSTRUCTION COST				
				ENTIRE PROJECT	YOUR FIRMS RESPONSIBILITY			
Concrete Testing And Inspections	Testing and Inspections	Antero Resources, Bear Contracting, City of Buckhannon, Wolfe's Excavating	Ongoing	Varies	Varies			
Paving Projects Numerous	Testing and Inspections	Wolfe Excavating Bear Contracting Mountaineer Contractors Stantec	Ongoing	Varies	Varies			
Bartlett House	Site Plan for new structure	Bartlett House 1110 University Ave Morgantown, WV 26505	September 2020	Unknown	\$50,000			
ND Paper - various projects	Structure engineering and mechanical component drawings	ND Paper 702 AFR Drive Fairmont, WV 26554	Ongoing	\$40,000,000	Varies			
Ridgedale Retaining Wall	Retaining Wall Design and detailing	Monongalia County Schools	Just completed	Unknown	\$50,000			

17. COMPLETED WORK WITHIN LAS	T 5 YEARS ON WHICH YOUR FIRM W	AS THE DESIGNATED ENGINEER OF RECO	RD	
PROJECT NAME, TYPE AND LOCATION	NAME AND ADDRESS OF OWNER	ESTIMATED CONSTRUCTION COST	YEAR	CONSTRUCTED (YES OR NO)
Fort Martin Road Maintenance Monongalia County, WV & turning lane/entry improvements	Longview Power 1375 Fort Martin Rd Maidsville, WV 26541	\$125,00 & \$600,000	2018/2019	YES YES
Lowndes Hill Slip Repair Harrison County, WV	City of Clarksburg 222 West Main Street Clarksburg, WV 26301	\$200,000	2018	YES
The Vale, Residential Housing, Bridgeport, WV	Trailhead Investments, LLC. 721 Brightridge Drive Bridgeport, WV 26330	\$1,900,000	2018- 2019	YES
Realisations 789, AMD Treatment, Hancock County WV	Vesuvius 250 Parkwest Drive Pittsburgh PA	\$1,500,000	2018-2020	YES
Camden Slip Repair & Drainage Improvements	Mountain V Oil and Gas Bridgeport, WV	\$500,000	2020	YES
TL 255 Natural Gas replacement, 5 mile replacement, Wood County WV	Dominion Energy Transmission Southern Regional Headquarters, Weston, WV	\$9,900,000	2020	YES
Sole/Morris Compressor Station, 12 acre compressor pad for natural gas operations, Tyler County, WV	Antero Resources White Oaks Blvd. Bridgeport, WV	\$1,000,000	2019	YES
ND Paper Slip, repair of slip along Monongahela River, Marion County	ND Paper 702 AFR Drive Fairmont, WV 26554	\$500,000	2020	YES

18. COMPLETED WORK W	VITHIN LAST 5 YEARS ON WH	ICH YOUR FIRM HAS BEEN A SUB-CO	NSULTANT	TO OTHER FIRMS	(INDICATE PHASE
	CH YOUR FIRM WAS RESPONS	· · · · · · · · · · · · · · · · · · ·			
PROJECT NAME, TYPE	NAME AND ADDRESS	ESTIMATED CONSTRUCTION COST	YEAR	CONSTRUCTED	FIRM ASSOCIATED
AND LOCATION	OF OWNER	OF YOUR FIRM'S PORTION		(YES OR NO)	WITH
Leon Street Slip,	Town of Clarksburg, WV	\$1,000,000	2021	Design	Desmone
AML grant funded,				Complete	Architecture
Clarksburg WV					
WVU Hospitals	WVU Hospitals	\$500,000	2019	NO	Paradigm
Rehab Center	nespisais	1			Architecture
		information or description of r			
		st Virginia Abandoned Mine Land			
		ve a wide variety of experience			
		l as with our clientele, often			
		o with inexperienced designers			
		inage which is very well suited			
	in valued subs that make	Geotechnical and Survey project	componen	ts seamless wit	th the rest of our
operations.					
20 mbo formarian in	2 0+0+0m0n+ 25 522+2				
20. The foregoing is	a statement of facts.				
Signature:		Ti+le•		Date:	
Signature		Title:		Date	
Printed Name:					
					

ATTACHMENT B

AML and RELATED PRO	AML and RELATED PROJECT EXPERIENCE MATRIX																						
			PROJECT EXPERIENCE REQUIREMENTS												TCIPATI //=Manag		PACITY P=Prof	fession	*** al				
PROJECT	Exp. Basis C=Corp. P=Personnel	Additional Info Provided in Section (s)	Abandoned Surface Mine Reclamation	Abandoned Deep Mine Reclamation	Portal/Shaft Closure	Hydrologic/Hydraulic Design/Eval.	Remining Evaluation	Mine/Refuse Fire Abatement	Subsidence Investigation Mitigation	Hazardous Waste Disposal	Project Specifications	Water Quality Evaluation/Nitigation/ Replacement	Construction Inspection/Managem ent	Water Treatment	Eq;uipment/Structure Removal	Stream Restoration	Geotechnical/Stability	Michael Nestor	Eric Short	Jeff Knepper	Zachary Assaro	Devon Shrewsberry	Keith Axton
Anglins Run - AML	P		x	x	x	x					X						x	Р	P				
Roaring Creek - AML	P		х	х	x	х			x		x					x	x	P	P				
Lowndes Hill Slip Repair	C/P		x						x		x		x				x	M/P	Р		P		
Leon Street Slip Repair - AML	C/P		x	x		x	_		x				x			x	x	M	Р	P		Р	Р
Vesuvious Clay Mine	C/P		х	х	x	х		x	x	x		x	x	х	x	х				M/P	M	_	
Shiloh Development	C/P		x	x		x	_	x	x		x	x	x			x	x	M/P	Р	P			Р

^{*} List whether project experience is corporate or personnel based or both.

Attachment "A"

^{**} Use this area to provide specific sections or pages if needed for reference.

^{***} List Primary Design personnel and their functional capacity for the projects listed.

ATTACHMENT C



REGISTRATIONS

Professional Engineer:

- West Virginia
- Virginia,
- Ohio
- Pennsylvania
- Maryland

ASSOCIATIONS

- American Society of Civil Engineers.
- American Society of Highway Engineers (Past President of NCWV Region).

EDUCATION

Fairmont State College, Fairmont, WV

Bachelor of Science in Engineering Technology

YEARS EXPERIENCE

- 16 years
- 2 ½ years at ACE

Email:

mike@ascentconsultingengineers.com

MICHAEL NESTOR, PE

SUMMARY

Mr. Nestor is a Civil Engineer registered professionally in WV and serves as the Managing Member of Ascent Consulting and Engineering, LLC. He has over 16 years of consulting experience focusing on land development projects and stormwater management in WV, MD, and PA. His expertise allows him to guide projects from concept to completion by understanding the goals/vision of the project, effectively communicating with the project team, and paying careful attention to the details. Mr. Nestor will be responsible for leading and client communication on this project.

EXPERIENCE

ASCENT CONSULTING AND ENGINEERING, (CLARKSBURG, WV)

Mr. Nestor is the founding/managing member of Ascent. He is responsible for the day to day operations of the firm and Quality Assurance/Control. In addition, Mike serves as the Engineering Division Manager, working with Engineers, CAD Techs, etc. to ensure projects include practical and efficient designs, and are delivered in a timely manner.

THE THRASHER GROUP, (BRIDGEPORT, WV)

Throughout Mr. Nestor's employment with The Thrasher Group, he served in a variety of roles ranging from Staff Engineer up to Site Group Division Manager. This allowed him to work on teams for a wide variety of projects and in a range of capacities.

BUSINESS AND INDSUSTRIAL PARKS

Designed and permitted the sites for multiple commercial and industrial properties ranging from major development projects such as the White Oaks Business Park and West Ridge Development to individual development sites for commercial and retail uses.

ROADS/SIDEWALKS

Designed and managed various roadway projects ranging from new road builds to maintenance and improvement projects.

STORMWATER MANAGEMENT

Designed numerous stormwater management facilities and developed stormwater management programs for compliance to the State of WV's MS4 Program in several communities.



REGISTRATIONS

- Certified Professional Geologist – Virginia
- Licensed Remediation
 Specialist West Virginia
- Certified Aboveground
- •Storage Tank Inspector STI-SP001
- Certified Aboveground
 Storage Tank Inspector –
 Pennsylvania

EDUCATION

West Virginia University, Morgantown, WV – Bachelor of Science in Geology –1998

ASSOCIATIONS

- American Institute of Professional Geologist
- West Virginia
- Manufacturers Association
- •IOGA of West Virginia
- •PIOGA PA

YEARS EXPERIENCE

- 20+ years
- 1 ½ years at ACE

Email:

jeffk@ascentconsultingengineers.com

JEFFREY KNEPPER, CPG, LRS

SUMMARY

Mr. Knepper has 20 years of experience working on complex environmental and regulatory projects specializing in environmental/regulatory compliance, remediation, permitting, and aboveground storage Tank (AST) services. Mr. Knepper is adept at developing practical and innovative solutions to challenging environmental issues often faced by oil and gas and other industrial clients. His track record in regulatory compliance, permitting, soil and groundwater remediation, and environmental impacts make him a key team member on projects. Mr. Knepper is a certified professional geologist and a WV licensed remediation specialist. Mr. Knepper is an experienced AST inspector with over 1,000 completed inspections in various states including: WV, PA, OH, KY, WI, MI, VA and NY.

EXPERIENCE

ENVIRONMENTAL INVESTIGATIONS

CPFilms, Industrial Facility, Fieldale, VA – Mr. Knepper performed nature and extent and site characterization studies for volatile organic compounds. He developed corrective action plans, installed groundwater monitoring wells and performed statistical analyses on results.

Federal Mogul, Industrial Facility, Winchester, VA – Mr. Knepper performed groundwater sampling and statistical analyses on results to determine the cause of upgradient groundwater contamination. Mr. Knepper received a commendation from the Virginia Department of Environmental Quality for exemplary sampling methods and techniques.

U.S. Silica, Berkeley Springs, WV – Mr. Knepper led the field operations team at an emergency spill cleanup for chemicals which included: sulfuric acid, caustic soda and petroleum sulfonate from aboveground storage tanks. Mr. Knepper's full knowledge of the WVDEP regulations for tanks and site cleanup proved invaluable in minimizing potential contamination and receiving high praise from the WVDEP.

ENVIRONMENTAL REGULATORY AND COMPLIANCE

Dominion Energy Transmission, Bridgeport, WV – Mr. Knepper developed a permitting guide to monitor permit conditions, permit expirations and regulatory deadlines. This guide encompassed all of Dominion's permits. It helped to mainstream and organize permits regardless of personnel responsibilities and turnover.

American Electric Power, Mountaineer Plant, New Haven, WV - Mr. Knepper developed the first Carbon Capture and Sequestration (CCS) permit in WV and the United States. The permit was issued prior to the Environmental Protection Agency releasing the regulations for the newly established class VI rules which now govern CCS.

UNDERGROUND INJECTION CONTROL

Mr. Knepper has over 10 years of experience working with underground injection control projects. He was the state-wide Environmental Resources Program Manager for WV handling all permitting and compliance approvals for mining facilities working closely with various mining companies including: Wolf Run Mining, Greenbrier Minerals, Independence Coal, Brooks Run Mining, Mid-Vol Coal Sales, Pinnacle Mining, ICG-Beckley, LLC and many more. Mr. Knepper has also provided this knowledge to the consulting realm as an alternative to existing permits or lack of efficiency in current treatment options.

Vesuvius, Globe Mine, Newell, WV – Mr. Knepper led a team to renew a NPDES permit at an old clay mine. The facility had been violation for many years because of the high concentration of iron. Mr. Knepper was instrumental in renewing the NPDES permit and providing an alternative to help bring the facility back into compliance with the WVDEP.

HYDROGEOLOGY

Georgia Pacific, Industrial Facility – Martinsville, VA - Mr. Knepper performed groundwater sampling and statistical analyses on volatile organic compounds, metals and semi-volatile organic compounds from groundwater samples.

Scott County, Gate City, VA – Mr. Knepper performed site characterization studies on volatile organic compounds contaminating multiple sites. Mr. Knepper prepared corrective action plans and nature and extent studies. He also performed groundwater statistics that were used by the VDEQ as a model for how to perform the various investigations and studies.

Patrick County, Stuart, VA – Mr. Knepper helped design and manage a gas extraction system for the County. He also was instrumental in the approval of a corrective action plan from the VDEQ for vinyl chloride contamination. Mr. Knepper developed alternatives the State of Virginia now uses to evaluate nature and extent studies and site characterization reports.



REGISTRATIONS

Pennsylvania,
West Virginia,
Virginia,
Ohio, PE

EDUCATION

Bachelor of Science Degree in Mining Engineering, The Pennsylvania State University at University Park, Pennsylvania, 1983.

Certification from ASFE, Fundamentals of Professional Practice Management Course, Magna Cum Laude, 1996.

Maryland Erosion and Sediment Control Certification No. March 30, 2016

CORE QUALIFICATIONS

Site Development
Municipal Infrastructure
Erosion Control Plans
Brownfields
Redevelopment
Regulatory Compliance
Environmental Permitting
Storm Water Management
Technical Writing
Cost Estimating
Construction Management

JEFFREY A. PAROBEK, PE

SUMMARY

Mr. Parobek is currently employed as a Engineering Manager: He is responsible for overview of technical aspects of project design, design coordination with clients and other members of the design team, public presentations of projects in front of governing bodies, regulatory agencies and at stakeholder meetings, coordination of project bid process and oversight of services during construction including change order and pay application reviews, coordination with other managers for manpower and scheduling, preparation of price proposals and statements of qualifications, preparation of invoices and supplemental work requests.

EXPERIENCE

Palomino Drive Water Line in Weirton, West Virginia for the City of Weirton, Dept. of Water. Water line extension project for a 14" water main (approximately 1,900 l.f.) to serve the Three Springs Industrial and Business Park.

Lardin Substation Expansion in German Township, Pennsylvania for Allegheny Power. Mr. Parobek was project Manager for the project that included including grading, landscape buffer, drainage improvements, erosion and sediment control plans and stormwater management report. The project included coordination meetings with the municipalities and attendance at zoning and planning hearings to obtain local approvals.

Lead project engineer on part of the Indonesia Transmission Line in Irian Jaya for P.T. Freeport Indonesia Company. Design project for a reliable 60-mile-long, 230 kV transmission line from an ocean port site through mangrove swamps to a mill in the mountains at elevation 9,000 ft. to supply power to the client's copper and gold mining operations. Responsible for design and coordination of one- mile underground segment of twin 230 kV to avoid flight path issues with final approach to major airport.

Loyalhanna Substation Expansion in Latrobe, Pennsylvania for Allegheny Power. A Site development project to expand the Loyalhanna Substation. Mr. Parobek was project manager for the site design portion of the project that consisted of topographic and property survey, grading plans and erosion and sediment control plans. The project also included coordination meetings with the municipality and local permitapplications.

Summerset at Frick Park Residential Development at Nine Mile Run in Pittsburgh, Pennsylvania for the Urban Redevelopment Authority of Pittsburgh. Residential development project for a 238- acre brownfield site requiring Phase I and II grading, infrastructure planning, design, and permitting for a 713-unit multi-phased residential development on an abandoned riverside slag dump bordering the main access highway to Pittsburgh's eastern suburbs.



EDUCATION

B.S. Environmental Studies: Fisheries & Wildlife

California University of Pennsylvania, 2014

YEARS EXPERIENCE

• 7+ Years

CERTIFICATIONS

- 10 Hour OSHA Construction & Health Certification, 2015
- 40-Hour Army Corps of Engineers Wetland Delineation Certification, Richard Chinn Environmental Training, 2015
- Morphological Soils Investigations Certification, PADEP, 2016
- Ohio Rapid Assessment Method for Wetlands v. 5.0 Training Course, 2017
- PADEP One-Day Technical Training, 2017
- Asbestos Building Inspector Certification – December 2021
- WV Licensed Asbestos Inspector Issued December 2021

ASSOCIATIONS

- Member of The Women's Energy Network WV
- University Relations Chair Air & Waste Management Association

Email:

megan@ascentconsultingengineers.com

MEGAN WAGNER ENVIRONMENTAL SCIENTIST

SUMMARY

Ms. Megan Wagner is an Environmental Scientist for Ascent services. Ms. Wagner has approximately 7 years of experience with data collection, report writing and GIS mapping for a variety of projects. Her experience includes stream and wetland delineations, soil assessments, infiltration testing, soil profiling, stream assessments and monitoring, BMP suitability reports, habitat assessments, permit writing, Phase 1 reporting, SWPPP, GPP, and SPCC plans, stormwater sampling, and GIS mapping/data processing. She is a certified Asbestos Inspector with a license in West Virginia. She has been involved in numerous projects located within WV, PA, and OH. The range of projects include, well pads, access roads, road upgrades, gathering lines, ASTs, impoundments, modifications, slip repairs, and water and gas pipeline projects.

EXPERIENCE

DIEFFENBAUCH & HRITZ

Environmental Scientist II, GIS Technician

Generated field work, data collection, and report writing for stream and wetland delineations. Completed nationwide permits and stream activity permits. Operated soil infiltration testing and subsurface evaluations for soil assessment reports. Performed rare, threatened, and endangered species studies and regulatory coordination, habitat assessment and plant relocation projects. Conducted stream assessment, monitoring, and macroinvertebrate surveys. Completed mapping, GIS, and GPS data with ArcGIS 10.6 and Trimble Geo 7x Units. Performed erosion and sediment control inspections.

SUTTON AVIAN RESEARCH CENTER

Survey Technician

Was responsible for collection of all field data on federally threatened Lesser Prairie Chicken. Performed habitat assessment based on vegetation and topography. Completed triangulation points for determined Leks. Utilized four-wheel drive on rough terrain/roads. Identified target species as well as multiple grassland birds.

ALLEGHENY WOOD PRODUCTS

Forestry Intern

Assisted forestry with research on the Blackwater Canyon Habitat Conservation Plan (HCP). Maximized research on Indiana bat, Northern long-eared bat, Virginia bat, and Cheat Mountain salamander for better understanding of endangered species present and to assist forestry on proposing a proper HCP to allow timber harvest on the Blackwater Canyon property.



EDUCATION

B.S. Biology

Waynesburg University, 2018

YEARS EXPERIENCE

4+ Years

CERTIFICATIONS/TRAINING

- Environmentally Sensitive
 Maintenance Certification- 2018
- Agricultural Conservation
 Technicians Bootcamp Level I- 2019
- NM Managing Nutrients Workshop- 2019
- NM Plan Writing Workshop- 2019
- NM Plan Review Workshop- 2019
- NM ACA & Manure Storage Workshop- 2019
- NM Stormwater & Soil Loss Workshop- 2019
- NM P Index Workshop- 2019
- Erosion and Sediment Control Plan Review Training- 2019
- Asbestos Building Inspector Certification – December 2021
- WV Licensed Asbestos Inspector Issued December 2021
- 38-Hour Army Corps of Engineers Wetland Delineation Certification, Richard Chinn Environmental Training, 2022

Email:

sara@ascentconsultingengineers.com

SARA HLATKY STAFF SCIENTIST

SUMMARY

Ms. Sara Hlatky is a Staff Scientist at Ascent services. Ms. Hlatky has approximately 4 years of experience with data collection, plan reviewing, plan writing and mapping for a variety of projects for earth disturbance and agriculture. She is a certified, licensed Asbestos Inspector in West Virginia. Her experience includes soil assessments, soil profiling, stream assessments and monitoring, BMPs for agriculture and earth disturbance, mapping, plan review, plan writing and data processing. She has been involved in numerous earth disturbance projects and agriculture planning projects located within PA. Range of projects include but not limited to DGLVR, slip repairs, well pads, commercial buildings, water and gas pipeline, rotational grazing, and ACA management.

EXPERIENCE

Greene County Conservation District Conservation Specialist

Managed and oversaw all District and District delegated programs at various levels. Programs include but not limited to: Agriculture, Nutrient Management, CH-102 Erosion and Sediment Control, CH-105 Water Obstructions and Encroachments, and DGLVR. Duties included: plan review, plan writing, soil sampling, E&S inspections. Managed the Districts' Greene County's Reinvestment in Agriculture Cost Share Enhancement Program (GRACE) program solely; the program promotes soil and water conservation through agriculture BMP implementation. Conducted all field and administrative work for GRACE.

Reliance Laboratories

Environmental Field Technician

Responsible for collection, sampling and environmental reporting of stormwater, wastewater and drinking water for government-regulatory entities, commercial and domestic clientele.


Waynesburg University Research

Abiotic and biotic impacts of acid mine drainage in Dunkard Creek-Greene County, PA

Conducted research on environmental impacts of acid mine drainage in Dunkard Creek, Greene County. Research involved stream monitoring, water sampling and macroinvertebrate surveying. Research was presented at two events: oral presentation at the Association of Southeastern Biologists 79th Annual Meeting in Myrtle Beach, SC and poster presentation at Waynesburg University's Research Symposium in Waynesburg, PA.

ATTACHMENT D

PROJECT TEAM

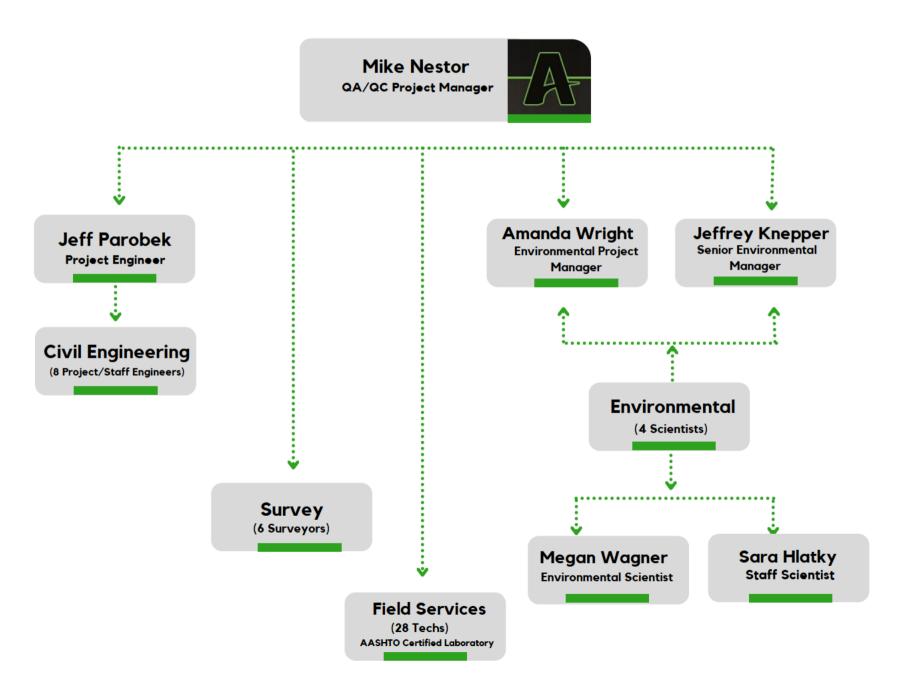

ATTACHMENT E



I, Mac Warner, Secretary of State of the State of West Virginia, hereby certify that

ASCENT CONSULTING AND ENGINEERING LLC

made application to the West Virginia Secretary of State's Office to be a registered limited liability company in the State of West Virginia on January 26, 2018. The application was received and found to conform to law.

The company is filed as an at-will company, for an indefinite period.

I further certify that the company has not been revoked or administratively dissolved by the State of West Virginia nor has the West Virginia Secretary of State issued a Certificate of Cancellation or Termination to the company.

Accordingly, I hereby issue this Certificate of Existence

CERTIFICATE OF EXISTENCE

Validation ID:3WV1G_DBDBQ

NEST VIANI SEMPER LIBERT

Given under my hand and the Great Seal of the State of West Virginia on this day of

Mac Warner

February 25, 2021

Secretary of State



west virginia department of environmental protection

Division of Land Restoration 601 57th Street SE Charleston, WV 25304 Harold D. Ward, Cabinet Secretary www.dep.wv.gov

October 13, 2021

Jeffrey Knepper Ascent Consulting & Engineering, LLC 2361 Davisson Run Road Clarksburg, WV 26301

Renewal - Licensed Remediation Specialist Certification

Dear Mr. Knepper:

Congratulations! We are pleased to inform you that you have filed your renewal application in accordance with appropriate time frames along with evidence of continuing education in the environmental remediation field. You have completed in a timely manner all of the license renewal requirements.

Please find your Licensed Remediation Specialist Renewed License Certificate enclosed and you may continue to practice as a licensed remediation specialist.

Sincerely,

Michael Sheehan Acting Director

Enclosure: LRS License Renewal Certificate

ec: LRS file: Registration Number

Renewal



West Virginia

Department of

Environmental Protection

KNEPPER, JEFFREY S
Licensed Remediation Specialist

Registration Number:

10/01/2021 - 09/30/2023

Date Issued - Date Expires



CONTRACTOR LICENSE

Authorized by the

West Virginia Contractor Licensing Board

Number:

WV058563

Classification:

GENERAL BUILDING

ASCENT CONSULTING AND ENGINEERING L DBA ASCENT CONSULTING AND ENGINEERING L 2361 DAVISSON RUN RD STE 103 CLARKSBURG, WV 26301

Date Issued

Expiration Date

MAY 08, 2021

MAY 08, 2022


Authorized Company Signature

Chair, West Virginia Contractor Licensing Board

This license, or a copy thereof, must be posted in a conspicuous place at every construction site where work is being performed. This license number must appear in all advertisements, on all bid submissions and on all fully executed and binding contracts. This license cannot be assigned or transferred by licensee. Issued under provisions of West Virginia Code, Chapter 21, Article 11.

COMMONWEALTH of VIRGINIA

EXPIRES ON 08-31-2023 Department of Professional and Occupational Regulation 9960 Mayland Drive, Suite 400, Richmond, VA 23233 Telephone: (804) 367-8500



BOARD FOR PROFESSIONAL SOIL SCIENTISTS, WETLAND PROFESSIONALS & GEOLOGISTS CERTIFIED PROFESSIONAL GEOLOGIST



Status can be verified at http://www.dpor.virginia.gov



(SEE REVERSE SIDE FOR PRIVILEGES AND INSTRUCTIONS)

DPOR-LIC (02/2017)

ATTACHMENT F

ABANDONEDMINELANDS(AML)CONTRACTORINFORMATIONFORM

You must complete this form for your AML contracting officer to request an eligibility evaluation from the Office of Surface Mining Reclamation and Enforcement (OSMRE) to determine if you are eligible to receive an AML contract. This requirement can be found under OSMRE's regulations at 30 CFR 874.16. **NOTE:** This form must be signed and **dated within 30 days** of submission to be considered for a current bid.

Part A: General Information

Business Name:	ascent Consulting and Engineering, LLC	
Tax ID#:	82-4069240	
Address:	2361 Davisson Run Rd. Suite 103	
City, State, & Zip:	Clarksburg, WV 26301	
Phone Number:	304-933-3465	_
Email Address:	tanya@ascenteonsultingengineers.com	
	, e	_

Part B: Obtain an Organizational Family Tree (OFT) from the Applicant Violator System (AVS)

If you plan to certify the existing AVS information or submit updates under Part C, you must include an OFT. Instructions for downloading an OFT from the AVS can be found at:

https://www.osmre.gov/resources/forms/OMB1029-0119instructions.pdf

If you require assistance you may contact the AVS Office by phone at: 800-643-9748, or by email at: avshelp@osmre.gov.

Part C: Certifying and updating information in the AVS

Select one of the options, follow the instructions for the selected option, sign, and date below.

I, , have express authority to certify that: (Print Name)

1. Our business is listed in the AVS. The information is accurate, complete, and up to date. (If you select this option, you must attach an Entity OFT from the AVS to this form). Do not complete Part D.

2. Our business is in the AVS. The information needs to be updated. (If you select this option, you must attach an Entity OFT from the AVS to this form). Complete Part D to provide the missing or corrected information.

Our business is not listed in the AVS. The information needs to be added. Complete Part D to provide the information.

<u>6-22-22</u> Date

Signature

Managing member.

Part D: OFT Information

Contractor's Business Name: Oscent Consulting a Engineering . W.

If the current Entity OFT information for your business is incomplete in the AVS, or if there is no information in the AVS for your business, you must provide all of the following information as it applies to your business. Please include additional copies of this page if the space below is not sufficient to capture all information.

- Every officer(President, VicePresident, Secretary, Treasurer, etc.);
- · All Directors, Partners, and Members;
- All persons performing a function similar to a Director;
- Every person or business that owns 10% or more of the voting stock in your business;
- Any other person(s) who has the ability to determine the manner in which the AML reclamation project is being conducted.
- Please list an end date for any person who is no longer with your business.

Name:	michael K. Nestor	Name:
Address:	2361 Daysson Run Rd Ste 103	Address:
City, State, Zip:	Chrisburg, WV 26301	City, State, Zip:
Begin Date:	Jan · 2018	Begin Date:
End Date:	NIA	End Date:
% Ownership:	50%	% Ownership:
Position/Title:	managing Member	Position/Title:
Phone Number:	304-933-3463	Phone Number:
Name:	Zachany Assaro	Name:
Address:	2361 Davison Run Rd. Stc 103	Address:
Address: City, State, Zip:	2361 Davison Run Rd. Stc 103 Clarksburg, WV 26301	
Address:	2361 Davison Run Rd. Stc 103	Address:
Address: City, State, Zip:	2361 Davison Run Rd. Stc 103 Clarksburg, WV 26301	Address: City, State, Zip:
Address: City, State, Zip: Begin Date:	2361 Davison Run Rd. Stc 103 Clarksburg, WV 26301	Address: City, State, Zip: Begin Date:
Address: City, State, Zip: Begin Date: End Date: % Ownership: Position/Title:	2361 Davison Run Rd. Stc 103 Clarksburg, WV 26301 May 2018 NIP	Address: City, State, Zip: Begin Date: End Date:

PAPERWORK REDUCTION STATEMENT

The Paperwork Reduction Act of 1995 (44 U.S.C 3501) requires us to inform you that: Federal Agencies may not conduct or sponsor, and a person is not required to respond to, a collection of information unless it displays a current valid 0MB control number. This information is necessary for all successful bidders prior to the distribution of AML funds, and is required to obtain a benefit.

Public reporting burden for this form is estimated to range from 15 minutes to one hour, with an average of 30 minutes per response, including time for reviewing instructions, gather and maintaining data, and completing and reviewing the form. You may direct comments regarding the burden estimate or any other aspect of this form to the Information Collection Clearance Officer, Office of Surface Mining Reclamation and Enforcement, 1849 C Street, NW, Room 4559, Washington, DC 20240.

STATE OF WEST VIRGINIA Purchasing Division

PURCHASING AFFIDAVIT

CONSTRUCTION CONTRACTS: Under W. Va. Code § 5-22-1(i), the contracting public entity shall not award a construction contract to any bidder that is known to be in default on any monetary obligation owed to the state or a political subdivision of the state, including, but not limited to, obligations related to payroll taxes, property taxes, sales and use taxes, fire service fees, or other fines or fees.

ALL CONTRACTS: Under W. Va. Code §5A-3-10a, no contract or renewal of any contract may be awarded by the state or any of its political subdivisions to any vendor or prospective vendor when the vendor or prospective vendor or a related party to the vendor or prospective vendor is a debtor and: (1) the debt owed is an amount greater than one thousand dollars in the aggregate; or (2) the debtor is in employer default.

EXCEPTION: The prohibition listed above does not apply where a vendor has contested any tax administered pursuant to chapter eleven of the W. Va. Code, workers' compensation premium, permit fee or environmental fee or assessment and the matter has not become final or where the vendor has entered into a payment plan or agreement and the vendor is not in default of any of the provisions of such plan or agreement.

DEFINITIONS:

"Debt" means any assessment, premium, penalty, fine, tax or other amount of money owed to the state or any of its political subdivisions because of a judgment, fine, permit violation, license assessment, defaulted workers' compensation premium, penalty or other assessment presently delinquent or due and required to be paid to the state or any of its political subdivisions, including any interest or additional penalties accrued thereon.

"Employer default" means having an outstanding balance or liability to the old fund or to the uninsured employers' fund or being in policy default, as defined in W. Va. Code § 23-2c-2, failure to maintain mandatory workers' compensation coverage, or failure to fully meet its obligations as a workers' compensation self-insured employer. An employer is not in employer default if it has entered into a repayment agreement with the Insurance Commissioner and remains in compliance with the obligations under the repayment agreement.

"Related party" means a party, whether an individual, corporation, partnership, association, limited liability company or any other form or business association or other entity whatsoever, related to any vendor by blood, marriage, ownership or contract through which the party has a relationship of ownership or other interest with the vendor so that the party will actually or by effect receive or control a portion of the benefit, profit or other consideration from performance of a vendor contract with the party receiving an amount that meets or exceed five percent of the total contract amount.

AFFIRMATION: By signing this form, the vendor's authorized signer affirms and acknowledges under penalty of law for false swearing (*W. Va. Code* §61-5-3) that: (1) for construction contracts, the vendor is not in default on any monetary obligation owed to the state or a political subdivision of the state, and (2) for all other contracts, that neither vendor nor any related party owe a debt as defined above and that neither vendor nor any related party are in employer default as defined above, unless the debt or employer default is permitted under the exception above.

WITNESS THE FOLLOWING SIGNATURE: Vendor's Name: Ascent Consulting and Engineering, LLC Authorized Signature: Date: 4/5/2022 State of West Virginia County of Harrison , to-wit: Taken, subscribed, and sworn to before me this 5th day of April , 2022. My Commission expires May 30 , 2026 AFFIX SEAL HERE OFFICIAL SEAL NOTARY PUBLIC STATE OF WEST VIRGINIA

John E Robinson Jr. 401 Maryland Avenue Nutter Fort, WV 26301 My Commission Expires May 30, 2026 Purchasing Affidavit (Revised 01/19/2018)

DESIGNATED CONTACT: Vendor appoints the individual identified in this Section as the Contract Administrator and the initial point of contact for matters relating to this Contract.
Will Managing Member
(Name, Title)
Michael R. Nestor, Managing Member
(Printed Name and Title)
2361 Davisson Run Rd Suite 103
(Address)
Clarksburg, WV 26301
(Phone Number) / (Fax Number)
amanda@ascentconsultingengineers.com
(email address)
CERTIFICATION AND SIGNATURE: By signing below, or submitting documentation through wvOASIS, I certify that: I have reviewed this Solicitation in its entirety; that I understand the requirements, terms and conditions, and other information contained herein; that this bid, offer or proposal constitutes an offer to the State that cannot be unilaterally withdrawn; that the product or service proposed meets the mandatory requirements contained in the Solicitation for that product or service, unless otherwise stated herein; that the Vendor accepts the terms and conditions contained in the Solicitation, unless otherwise stated herein; that I am submitting this bid, offer or proposal for review and consideration; that I am authorized by the vendor to execute and submit this bid, offer, or proposal, or any documents related thereto on vendor's behalf; that I am authorized to bind the vendor in a contractual relationship; and that to the best of my knowledge, the vendor has properly registered with any State agency that may require registration. By signing below, I further certify that I understand this Contract is subject to the provisions of West Virginia Code § 5A-3-62, which automatically voids certain contract clauses that violate State law.
Ascent Consulting and Engineering, LLC
(Company)
(Company)
Managina Member
(Authorized Signature) (B.
(Authorized Signature) (Representative Name, Title)
Michael R. Nestor, Managing Member
(Printed Name and Title of Authorized Representative)
(Times Time of Aumorized Representative)
4/5/2022
(Date)
304-933-3463

(Phone Number) (Fax Number)
